


Pompano Fire Station 61																	
ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	% Complete	S	W	Oct 18, '20	S	T	M	F	Nov 1, '20	T
1			Permitting	1 day	Mon 11/16/20	Mon 11/16/20		100%									
2			Permitted Plans issued for use	1 day	Wed 10/14/20	Wed 10/14/20		100%									
3			Submittals & Long Lead Items	306 days	Wed 7/29/20	Thu 7/1/21		47%									
4			Shell and Site Submittals	150 days	Wed 7/29/20	Wed 2/3/21		80%									
5			MEP and Fire related Submittals	120 days	Mon 11/2/20	Fri 3/19/21		40%									
6			Elevator procurement	100 days	Mon 10/19/20	Thu 2/25/21		70%									
7			Exterior Windows, Doors & Store Front Procurement	90 days	Mon 11/9/20	Wed 2/24/21		75%									
8			Roofing Submittal	60 days	Mon 11/16/20	Sat 1/30/21		0%									
9			Genrator Submittal	100 days	Mon 11/16/20	Mon 3/1/21		80%									
10			Lighting Submittals	90 days	Mon 11/16/20	Sat 2/13/21		100%									
11			Interior finishes Submittals	60 days	Mon 3/1/21	Thu 4/29/21		15%									
12			Furniture including all locker and storage Submittals	90 days	Mon 1/4/21	Sat 4/3/21		0%									
13			Site Amenity Submittals	60 days	Mon 5/3/21	Thu 7/1/21		0%									
14			Remaining Submittals	200 days	Mon 11/16/20	Thu 6/3/21		20%									
15			Construction	300 days	Mon 11/16/20	Sat 9/11/21		7%									
16			Excavate, form, and pour footers	45 days	Mon 11/16/20	Wed 12/30/20		85%									
17			Shell including S.O.G., C.M.U., C.I.P	60 days	Mon 1/4/21	Thu 3/4/21		20%									
18			Trusses and metal decking	20 days	Fri 3/5/21	Wed 3/24/21		0%									
19			1st floor interior framing	15 days	Thu 3/25/21	Thu 4/8/21	17	0%									
20			I.S.O./Plywood/Dry In sloped roof	30 days	Thu 3/25/21	Fri 4/23/21	18	0%									
21			Roof inspection	1 day	Mon 4/26/21	Mon 4/26/21		0%									
22			2nd floor framing	15 days	Fri 4/9/21	Fri 4/23/21	19	0%									
23			1st Floor Electrical wall rough	15 days	Fri 4/9/21	Fri 4/23/21	19	0%									
24			1st Floor Plumbing Top Out	15 days	Fri 4/9/21	Fri 4/23/21	19	0%									
25			1st Floor HVAC Rough	15 days	Fri 4/9/21	Fri 4/23/21	19	0%									
26			1st Floor Fire Sprinkler Rough	20 days	Fri 4/9/21	Wed 4/28/21	19	0%									
27			Install windows and doors	10 days	Sat 4/24/21	Mon 5/3/21	20	0%									
28			Window Inspection	1 day	Tue 5/4/21	Tue 5/4/21	27	0%									
29			1st Floor exterior wall Insulation	5 days	Wed 5/5/21	Sun 5/9/21	28	0%									
30			Install Exterior H.M.D.	3 days	Wed 4/14/21	Fri 4/16/21	19FS+5 days	0%									
31			2nd Floor Electrical wall rough	15 days	Sat 4/24/21	Sat 5/8/21	23,22	0%									
32			2nd Floor Plumbing Top out	15 days	Sat 4/24/21	Sat 5/8/21	24,22	0%									
33			2nd Floor HVAC Rough	15 days	Sat 4/24/21	Sat 5/8/21	25,22	0%									
34			Wire Lath & Bead work Exterior only	10 days	Tue 5/4/21	Thu 5/13/21	27	0%									
35			Install Mechanical Well structural steel supports	2 days	Mon 4/26/21	Tue 4/27/21		0%									
36			Install waterproofing @ front upper deck	3 days	Wed 4/28/21	Fri 4/30/21		0%									
Project: Fire Station 61 Schedul Date: &[1/15/21]			Task Split Milestone Summary Project Summary Inactive Task Inactive Milestone Inactive Summary Manual Task Duration-only Manual Summary Rollup Manual Summary Inactive Summary Manual Task Duration-only External Milestone Deadline Critical Critical Split Progress														
Page 1																	




Pompano Fire Station 61

W | May 2, '21 | S | T | M | F | May 16, '21 | T | S | W | May 30, '21 | S | T | M | F | Jun 13, '21 | T | S | W | Jun 27, '21 | S | T | M | F | Jul 11, '21 | T | S | W | Jul 25, '21 | S | T | M | F | Aug 8, '21 | T | S | W | Aug 22, '21 | S | T | M | F | Sep 5, '21 | T | S | W | Sep 19, '21 | S | T | M | F | Oct 3, '21 | T | S | W | C

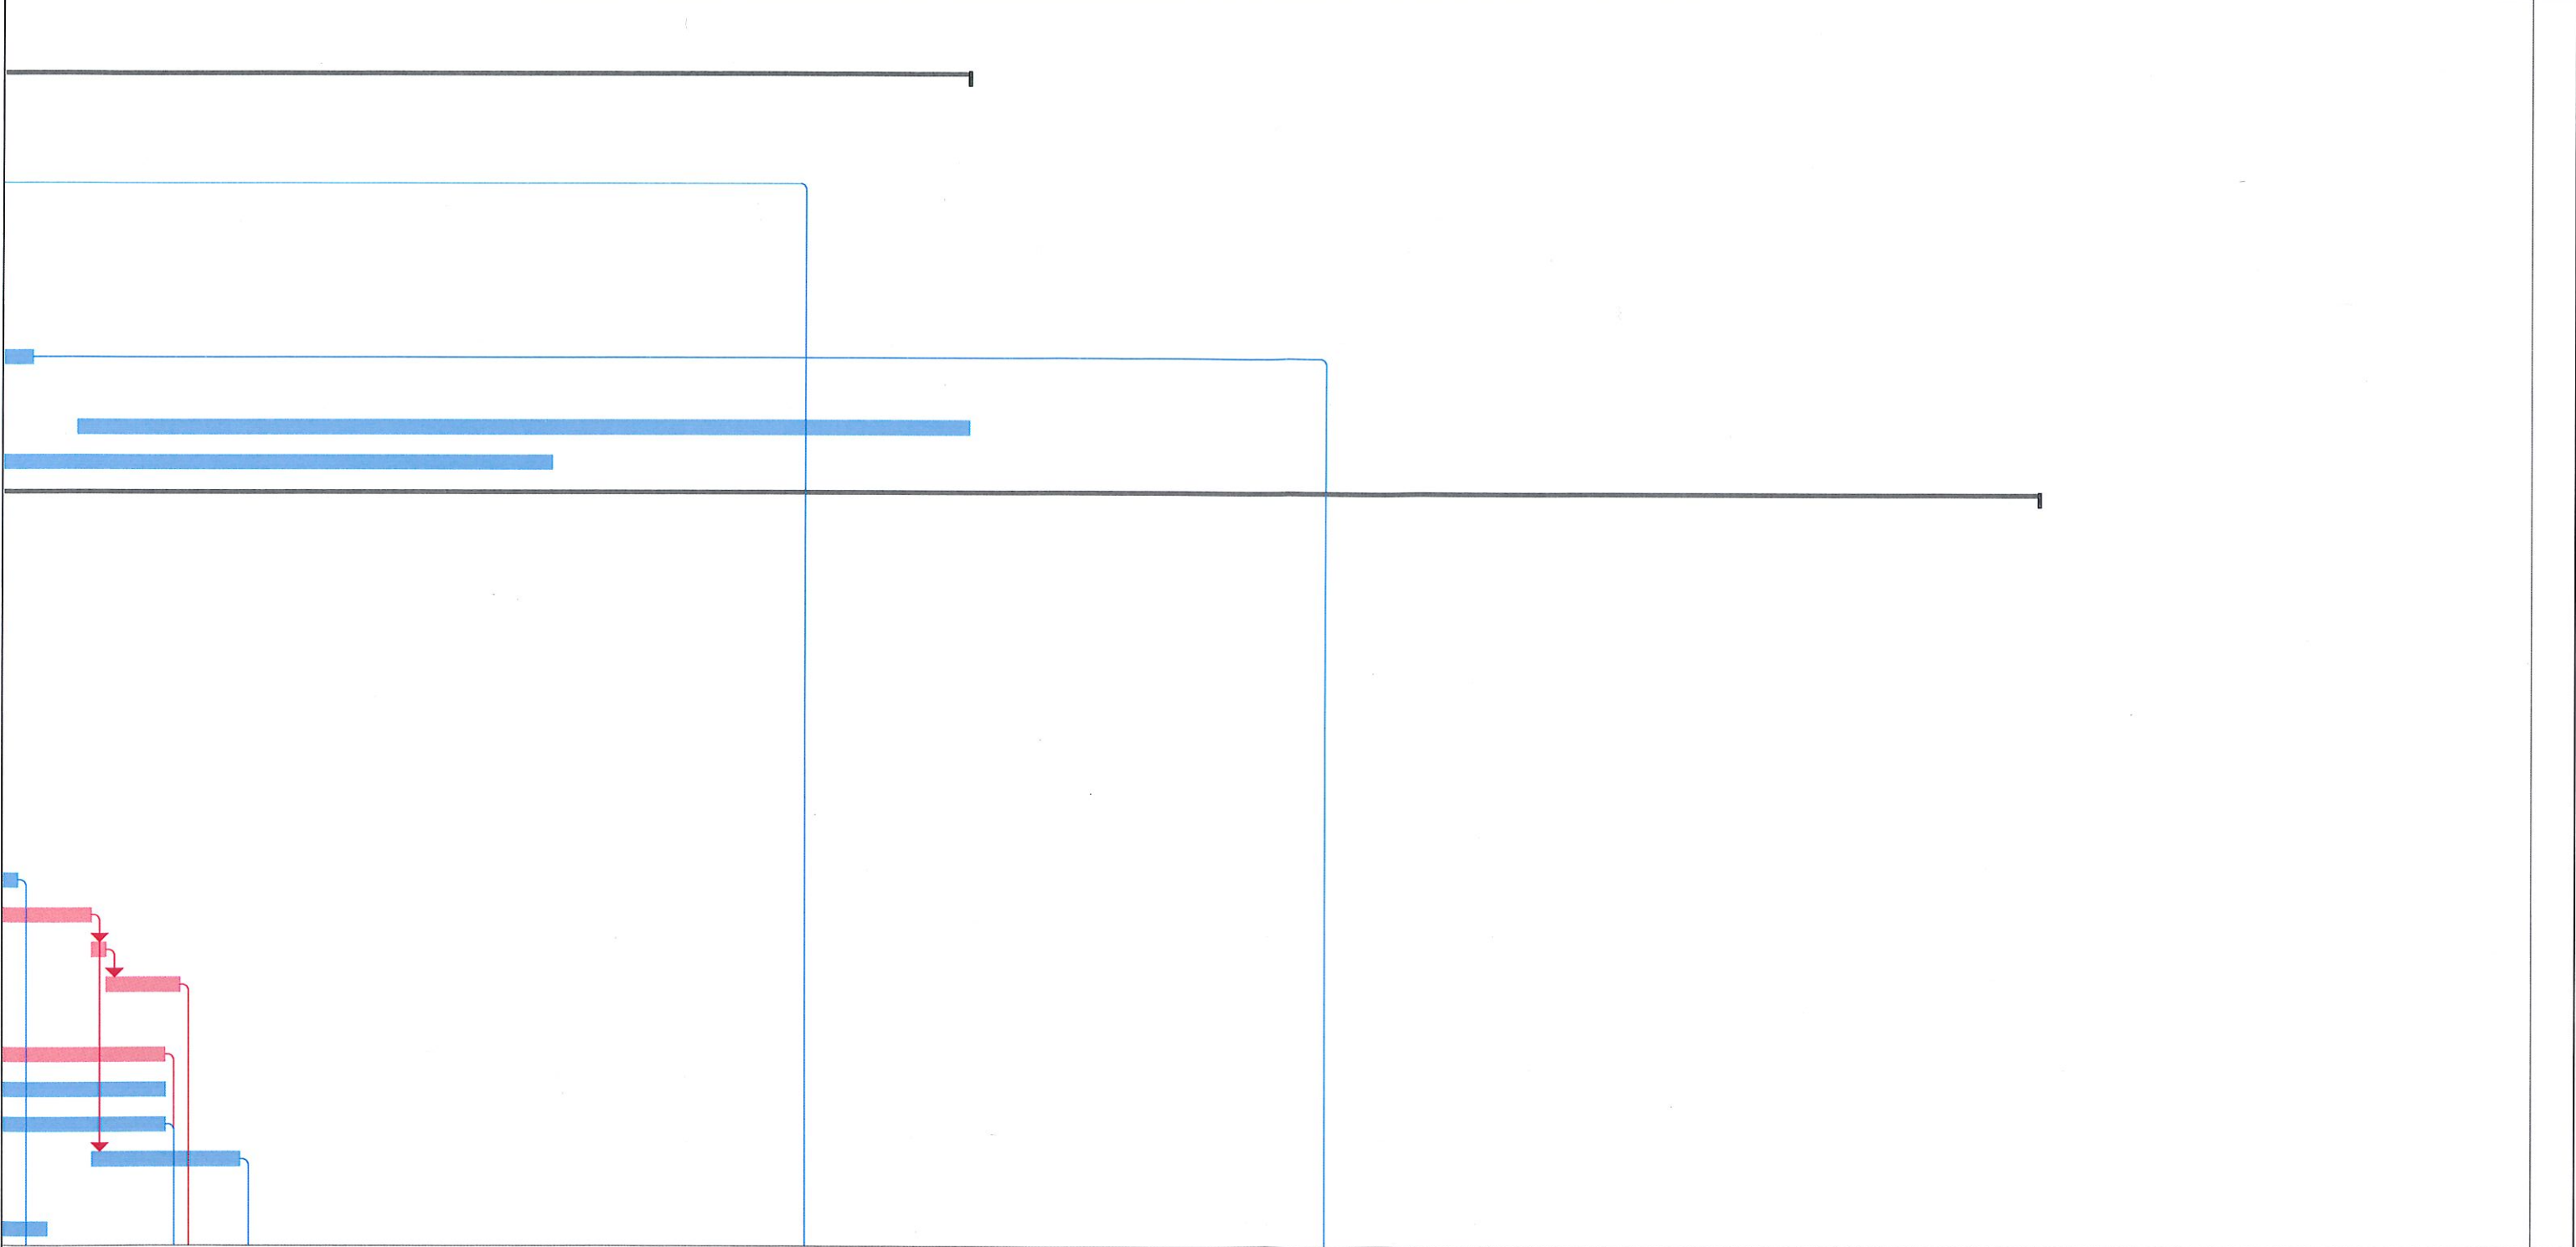


Project: Fire Station 61 Schedule Date: &[1/15/21]	Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
	Split		Inactive Milestone		Manual Summary		Deadline			
	Milestone		Inactive Summary		Start-only		Critical			
	Summary		Manual Task		Finish-only		Critical Split			
	Project Summary		Duration-only		External Tasks		Progress			

Pompano Fire Station 61

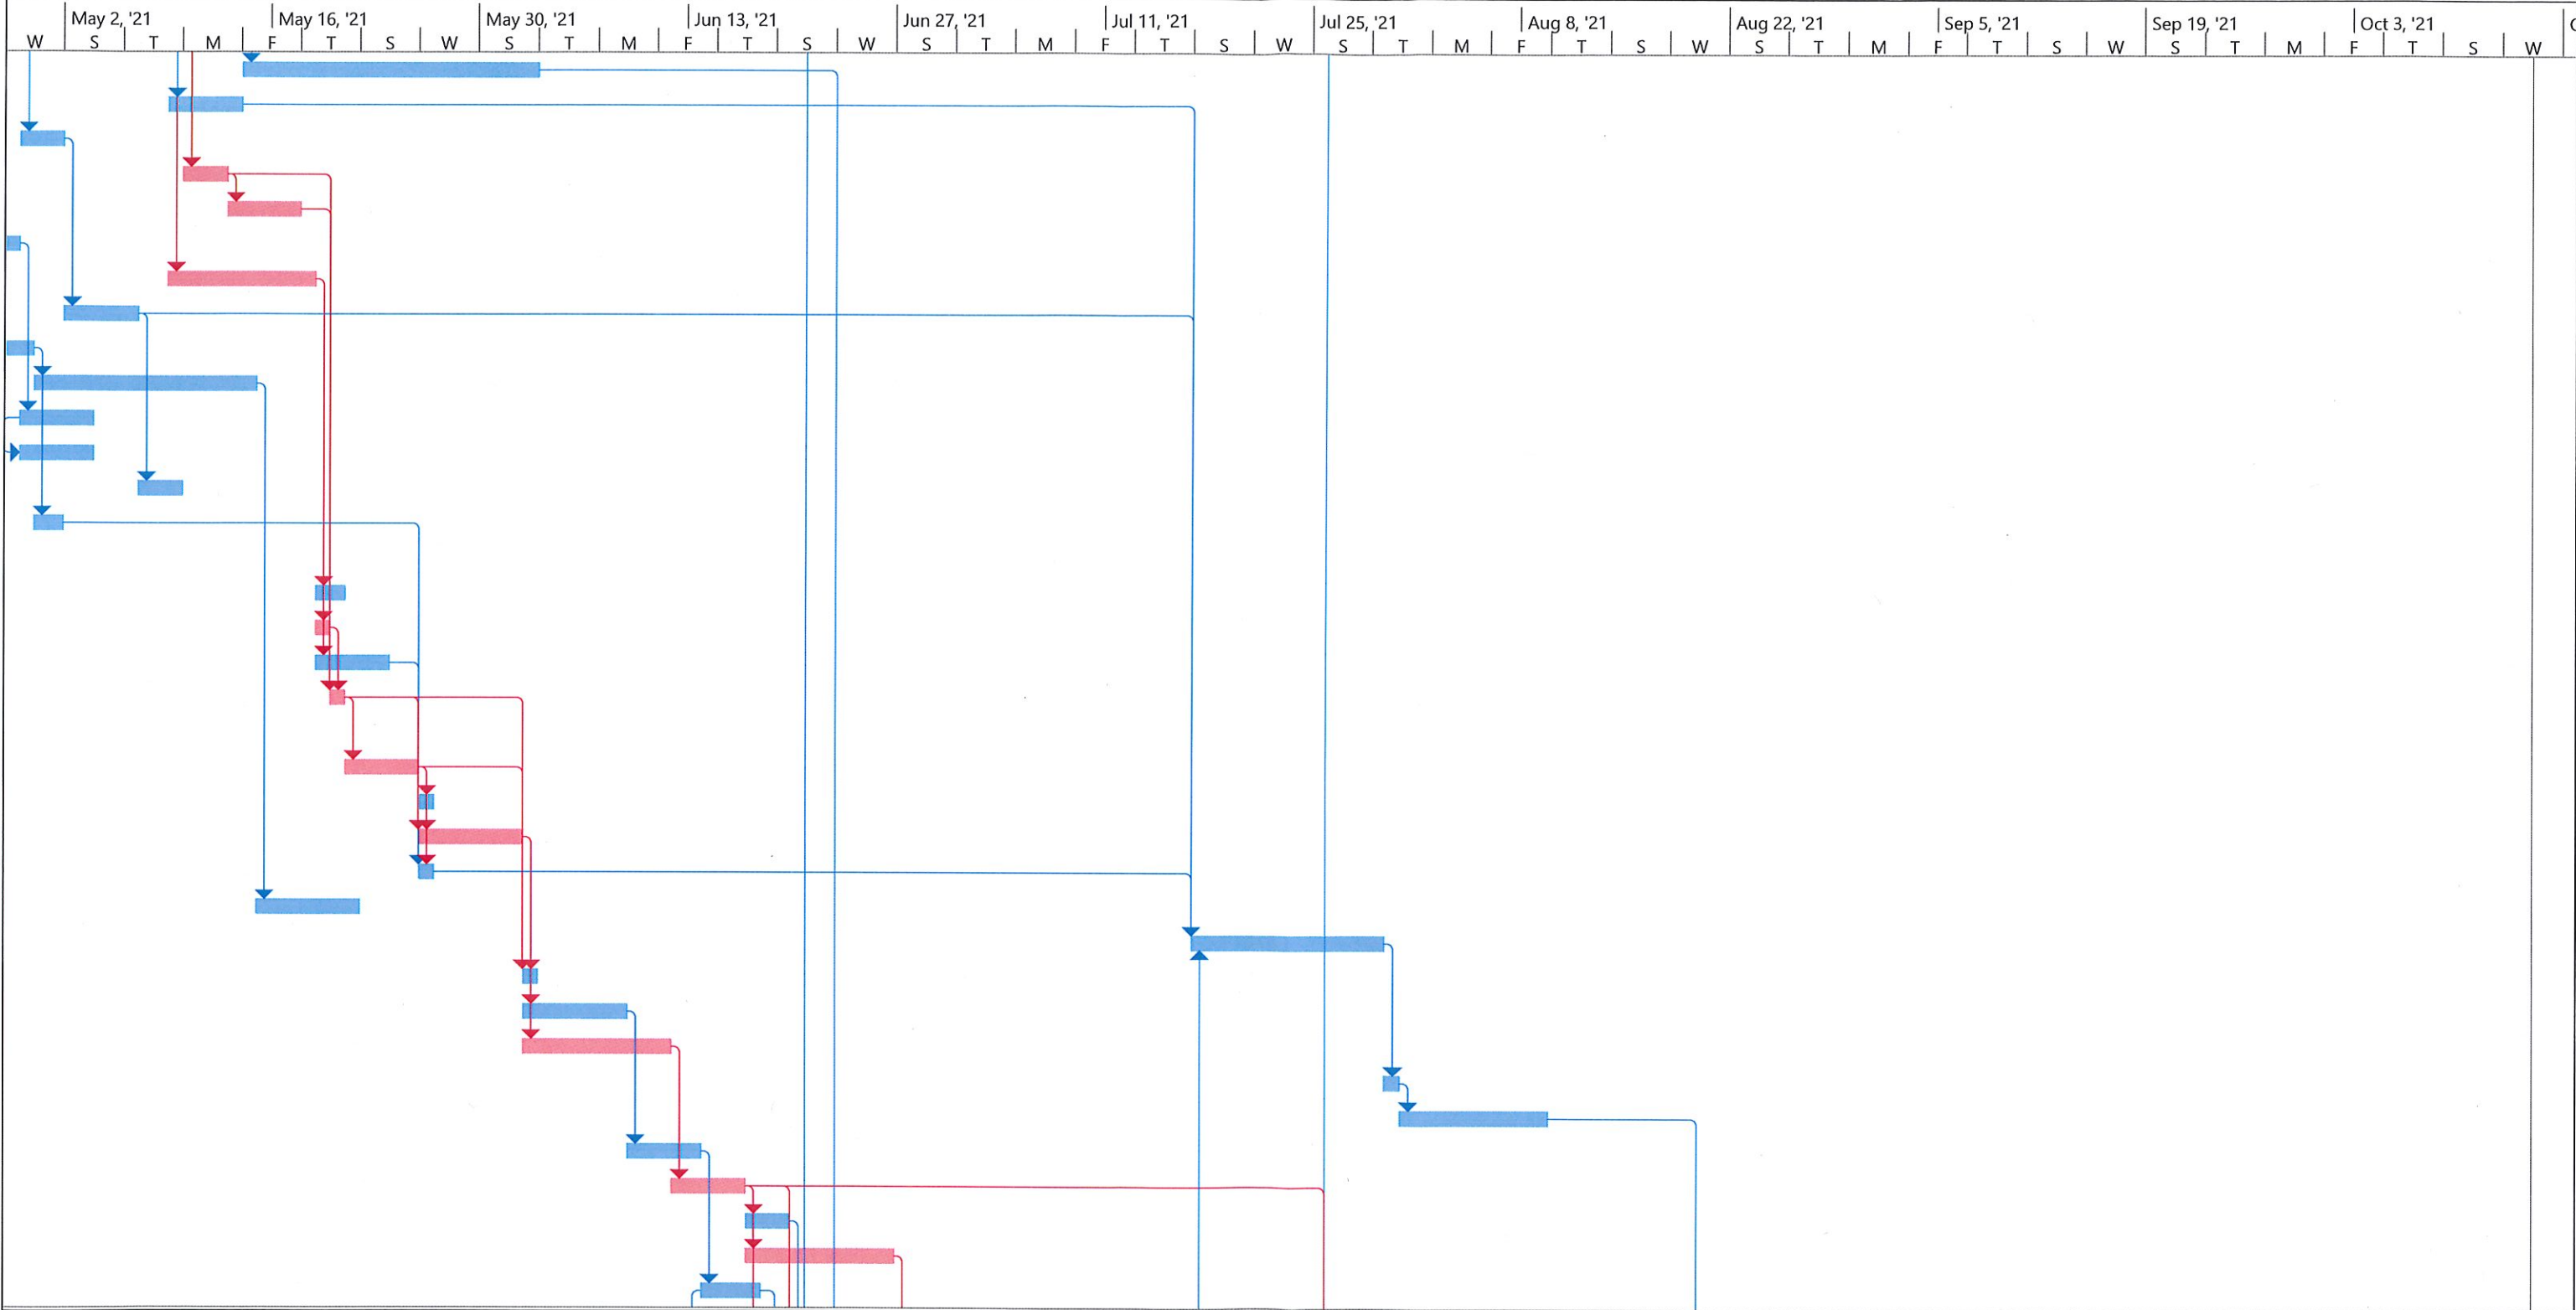

Project: Fire Station 61 Schedul
Date: &[1/15/21]

Pompano Fire Station 61

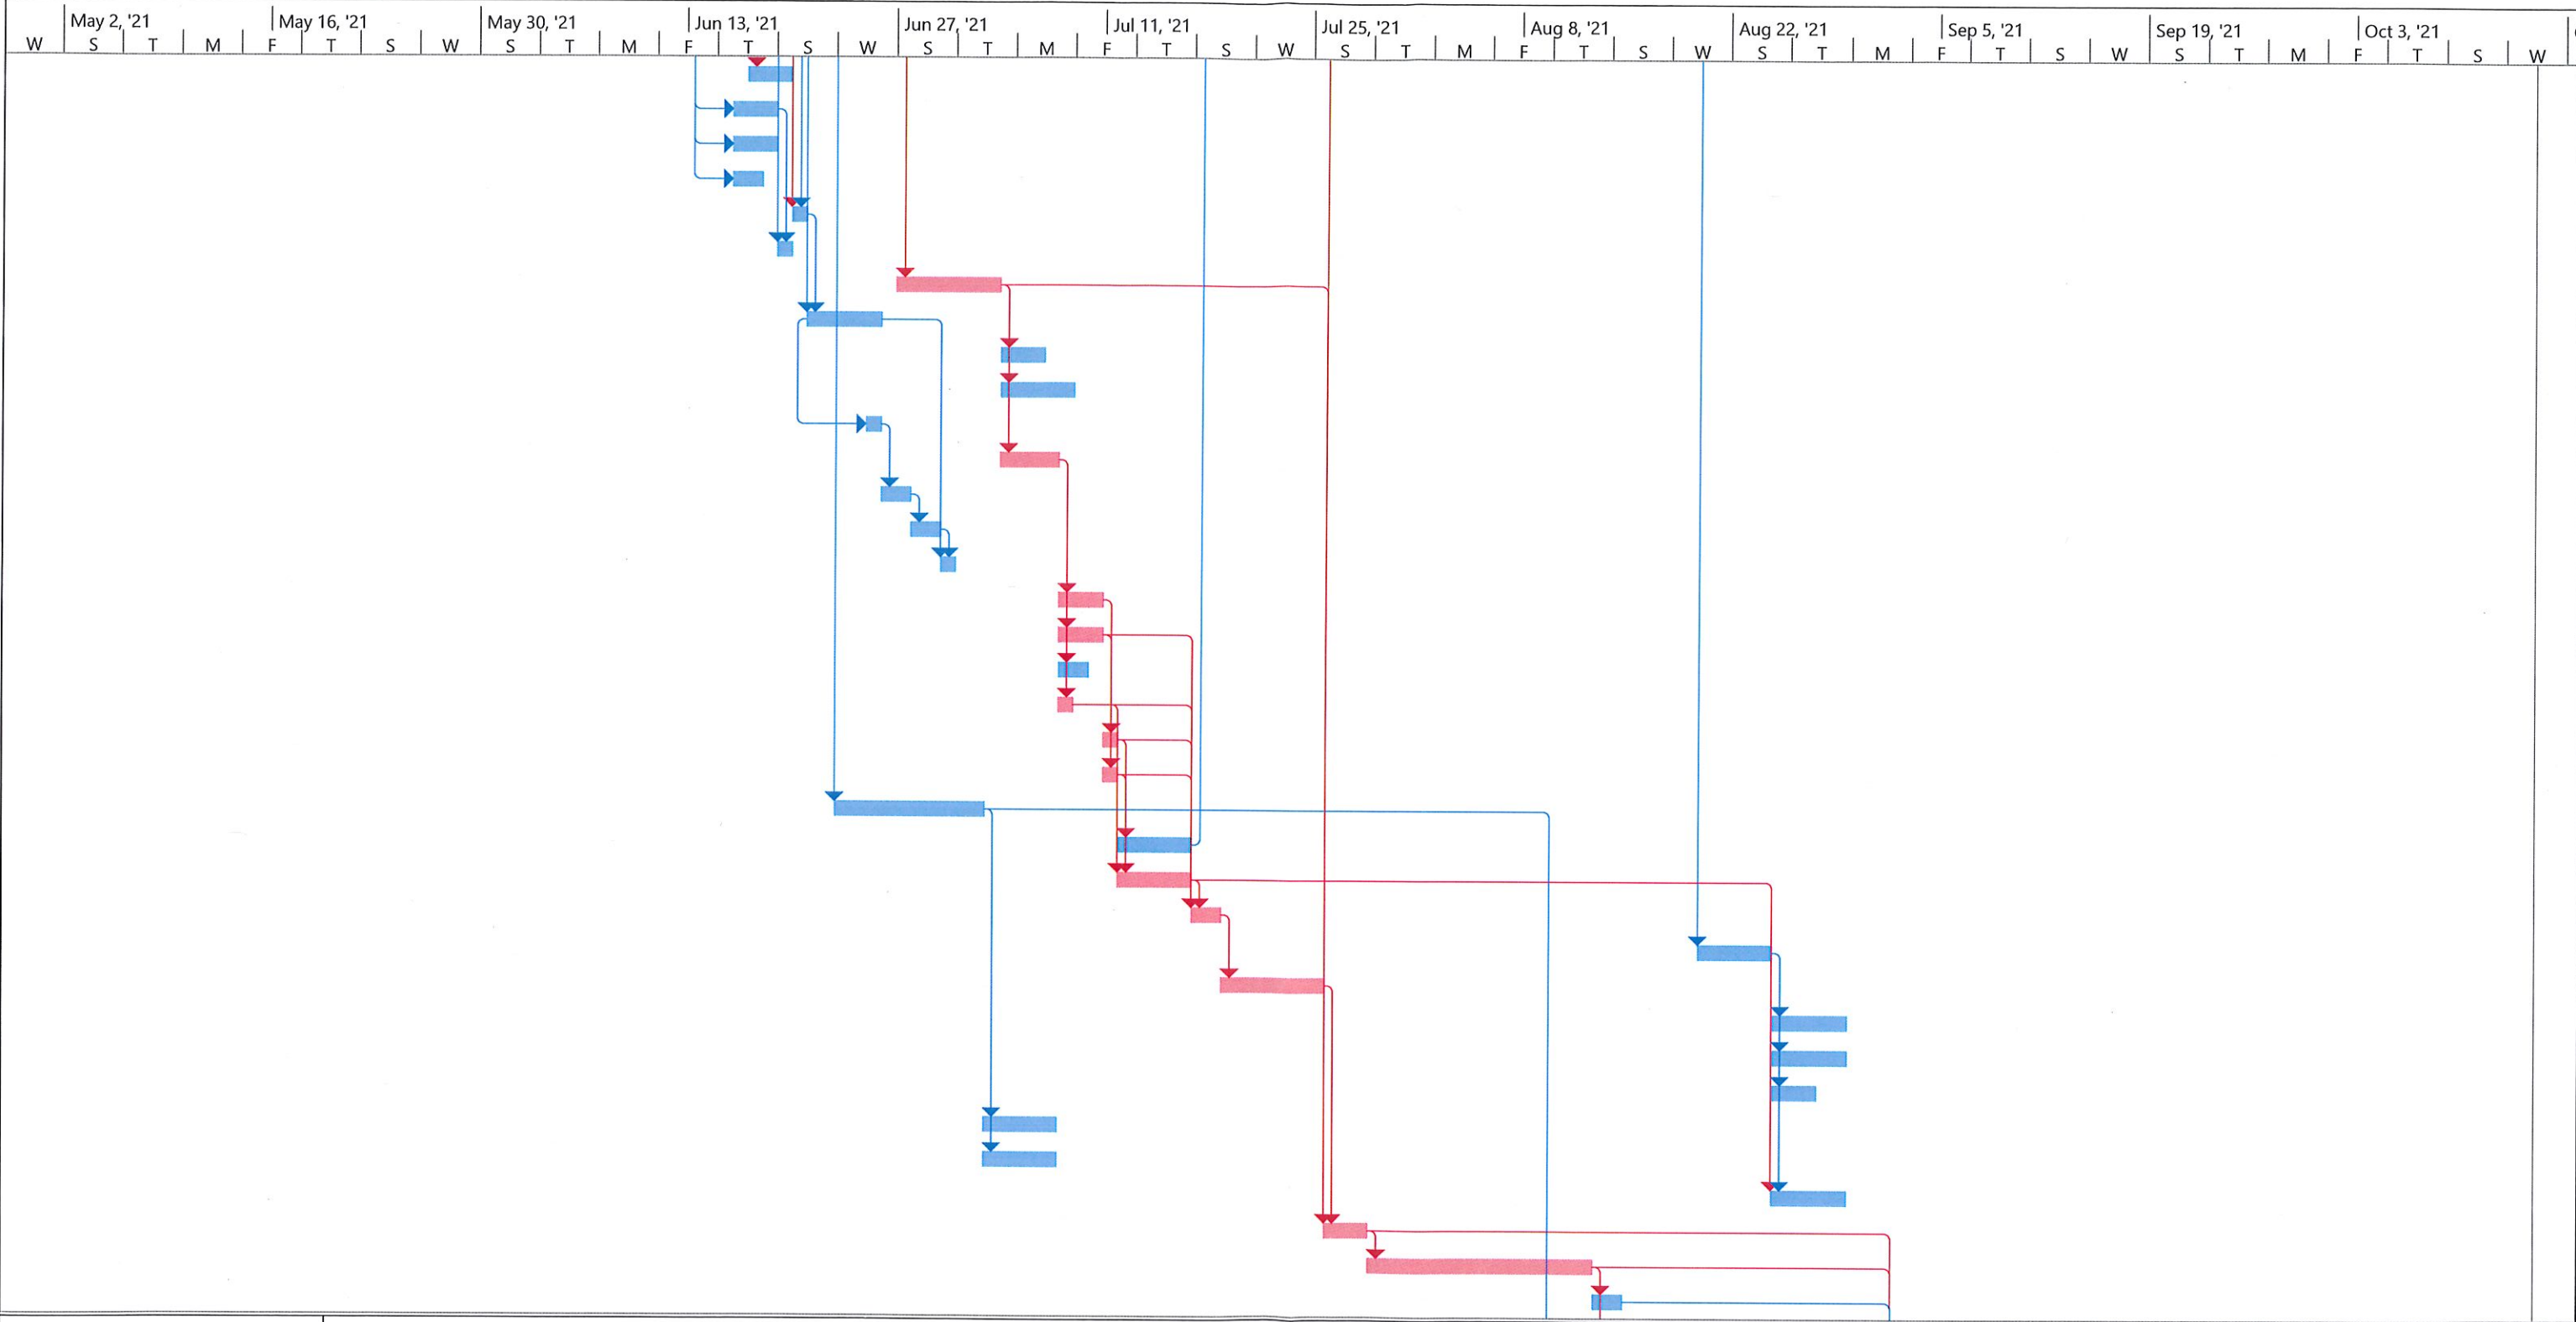

Project: Fire Station 61 Schedule Date: &[1/15/21]	Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
	Split		Inactive Milestone		Manual Summary		Deadline			
	Milestone		Inactive Summary		Start-only		Critical			
	Summary		Manual Task		Finish-only		Critical Split			
	Project Summary		Duration-only		External Tasks		Progress			

