

Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish	2020						2021														
						Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec		
Milestones												Milestones														
NTP	NTP Construction (Bldg Permit)-Bldg (Cal Days)	0	0	09-Dec-20A																						
SFND	StartFoundations-Bldg (Cal Days)	0	0	18-Mar-21																						
TOPOUT	TOPOUT-Bldg (Cal Days)	0	0		10-Jun-21																					
DRYIN-R	DRY-IN-Roof-Bldg (Cal Days)	0	0		14-Jul-21																					
TP-MS	Temp Power/Test-Bldg (Cal Days)	0	0		30-Aug-21																					
DRYIN	DRY-IN-Roofs/Windows-Bldg (Cal Days)	0	0		13-Sep-21																					
RINS	Framing/RIs Complete-Bldg (Cal Days)	0	0		01-Oct-21																					
PP-MS	Permanent Power-Bldg (Cal Days)	0	0		01-Oct-21																					
AC-MS	HVAC Startup-Bldg (Cal Days)	0	0		11-Oct-21																					
FIN	Finishes Complete-Bldg (Cal Days)	0	0		01-Nov-21																					
SCO-ACT	Substantial Completion-Actual-Bldg (Cal Days)	0	0		01-Nov-21*																					
DUR-ACT	Actual Duration to Substantial Completion (Cal Days)-Bldg	329	321	09-Dec-20A	01-Nov-21																					
C-DUR-REQ	Contract Duration to Substantial Completion (Cal Days)-Bldg	320	321	09-Dec-20A	01-Nov-21*																					
Precon												Precon														
Permitting												Permitting														
T-010	30% CD's	0	0	26-Jul-20A	26-Jul-20A																					
T-030	DRC Comments Issued	1	0	12-Aug-20A	12-Aug-20A																					
T-040	DRC Meeting	1	0	19-Aug-20A	19-Aug-20A																					
T-020	KL 30% Pricing Exercise	25	0	26-Jul-20A	28-Aug-20A																					
T-050	Sit-Down with CoPB for Line Item Review of Budget and DRC Comments	1	0	31-Aug-20A	31-Aug-20A																					
T-055	Permit Drawings	34	0	13-Aug-20A	15-Sep-20A																					
T-060	Permit Drawings issued to KL	1	0	16-Sep-20A	16-Sep-20A																					
T-080	Building Permit comments issued, sent to KL, KL addendum sent to bidders (1st round permit comments)	1	0	08-Oct-20A	08-Oct-20A																					
T-105	Revise Building Permit Drawings w/Comments	6	0	09-Oct-20A	21-Oct-20A																					
T-140	Submit Outside Agency Permit (1st round – 30 calendar days)	30	0	30-Sep-20A	30-Oct-20A																					
T-070	Submit for Building Dept Permit (1st round – 10 working days)	15	0	22-Oct-20A	10-Nov-20A																					
T-110	2nd Building Department Permit Submission	1	0	17-Nov-20A	17-Nov-20A																					
T-150	Outside Agency Permit Comments/Revise Drawings	7	0	02-Nov-20A	19-Nov-20A																					
T-160	2nd Round Outside Agency Permit Review (*Pending Removal of Hold from SFWMD)	30	0	20-Nov-20A	04-Dec-20A																					
T-115	2nd Round Building Department Review (10 working days)	14	0	18-Nov-20A	07-Dec-20A																					
T-170	Outside Agency Permit Received	0	0		15-Dec-20																					
T-180	3rd Round Building Department Review (10 working days)	10	1	07-Dec-20A	16-Dec-20																					
T-120	Building Permit Issued	1	1	17-Dec-20	17-Dec-20																					

■ Remaining Level of Effort ■ Critical Remaining Work
■ Actual Level of Effort ◆ Milestone
■ Actual Work — Summary
■ Remaining Work

McNair Park Project-15DEC20
 Progress Thru: 15-Dec-20
 File Name:MCN-15DEC20

Run Date: 15-Dec-20
 Data Date: 15-Dec-20
 Page 1 of 8



Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish	2020						2021											
						Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
Commission/GMP Approval		52	0	23-Sep-20A	08-Dec-20A	Commission/GMP Approval																	
T-090	KL GMP Pricing Exercise	15	0	23-Sep-20A	08-Oct-20A	KL GMP Pricing Exercise																	
T-091	CoPB PM Review	2	0	08-Oct-20A	09-Oct-20A	CoPB PM Review																	
T-092	CoPB Contract Mngr Addend. Preparation	3	0	12-Oct-20A	14-Oct-20A	CoPB Contract Mngr Addend. Preparation																	
T-093	CoPB PM Memo Prep	1	0	15-Oct-20A	15-Oct-20A	CoPB PM Memo Prep																	
T-094	CoPB Attorney Ordinance Prep	4	0	16-Oct-20A	21-Oct-20A	CoPB Attorney Ordinance Prep																	
T-097	CoPB Clerk Review	2	0	22-Oct-20A	23-Oct-20A	CoPB Clerk Review																	
T-098	Newspaper Ordinance Review	2	0	26-Oct-20A	27-Oct-20A	Newspaper Ordinance Review																	
T-096	Public Review Period	10	0	28-Oct-20A	06-Nov-20A	Public Review Period																	
T-095	Commission Mtg Lead Time	0	0	10-Nov-20A	10-Nov-20A	Commission Mtg Lead Time																	
T-100	Commission Ordinance Reading #1	1	0	17-Nov-20A	17-Nov-20A	Commission Ordinance Reading #1																	
T-101	Commission Reading #2 Lead Time	17	0	18-Nov-20A	07-Dec-20A	Commission Reading #2 Lead Time																	
T-130	Commission Ordinance Reading #2	1	0	08-Dec-20A	08-Dec-20A	Commission Ordinance Reading #2																	
Procurement		178	178	16-Dec-20	27-Aug-21	Procurement																	
Bid & Award Subcontracts		42	42	16-Dec-20	16-Feb-21	Bid & Award Subcontracts																	
P2910	Landscaping (Tree Removal)-Bid & Award Subcontracts	1	1	16-Dec-20	16-Dec-20	Landscaping (Tree Removal)-Bid & Award Subcontracts																	
P2200	Civil-Bid & Award Subcontracts	1	1	16-Dec-20	16-Dec-20	Civil-Bid & Award Subcontracts																	
P7850	Laminate Panel Ceiling-Bid & Award Subcontracts	3	3	16-Dec-20	18-Dec-20	Laminate Panel Ceiling-Bid & Award Subcontracts																	
P6170	Millwork-Bid & Award Subcontracts	3	3	16-Dec-20	18-Dec-20	Millwork-Bid & Award Subcontracts																	
P2855	Picket Fence-Bid & Award Subcontracts	3	3	16-Dec-20	18-Dec-20	Picket Fence-Bid & Award Subcontracts																	
P11020	Basketball Hoops-Bid & Award Subcontracts	3	3	16-Dec-20	18-Dec-20	Basketball Hoops-Bid & Award Subcontracts																	
P8250	OH Door-Bid & Award Subcontracts	3	3	16-Dec-20	18-Dec-20	OH Door-Bid & Award Subcontracts																	
P8100	HM Doors-Bid & Award Subcontracts	3	3	16-Dec-20	18-Dec-20	HM Doors-Bid & Award Subcontracts																	
P2500	Paving/Striping-Bid & Award Subcontracts	3	3	16-Dec-20	18-Dec-20	Paving/Striping-Bid & Award Subcontracts																	
P8400	Glass and Glazing-Bid & Award Subcontracts	3	3	16-Dec-20	18-Dec-20	Glass and Glazing-Bid & Award Subcontracts																	
P2920	Bleacher/Field Goal-Bid & Award Subcontracts	3	3	16-Dec-20	18-Dec-20	Bleacher/Field Goal-Bid & Award Subcontracts																	
P2950	Press Box-Bid & Award Subcontracts	3	3	16-Dec-20	18-Dec-20	Press Box-Bid & Award Subcontracts																	
P12000	Playground-Bid & Award Subcontracts	3	3	21-Dec-20	23-Dec-20	Playground-Bid & Award Subcontracts																	
P3000	Concrete Masonry-Bid & Award Subcontracts	3	3	21-Dec-20	23-Dec-20	Concrete Masonry-Bid & Award Subcontracts																	
P2930	Turf-Bid & Award Subcontracts	3	3	21-Dec-20	23-Dec-20	Turf-Bid & Award Subcontracts																	
P9000	Drywall/Ext Framing/Stucco-Bid & Award Subcontracts	3	3	28-Dec-20	30-Dec-20	Drywall/Ext Framing/Stucco-Bid & Award Subcontracts																	
P2050	Demo-Bid & Award Subcontracts	3	3	28-Dec-20	30-Dec-20	Demo-Bid & Award Subcontracts																	
P9900	Paint-Bid & Award Subcontracts	3	3	31-Dec-20	05-Jan-21	Paint-Bid & Award Subcontracts																	
P5000	Steel-Bid & Award Subcontracts	3	3	31-Dec-20	05-Jan-21	Steel-Bid & Award Subcontracts																	
P16500	Field Lighting-Bid & Award Subcontracts	3	3	06-Jan-21	08-Jan-21	Field Lighting-Bid & Award Subcontracts																	
P16000	Electrical Switchgear-Bid & Award Subcontracts	3	3	06-Jan-21	08-Jan-21	Electrical Switchgear-Bid & Award Subcontracts																	
P16010	Electrical Lighting-Bid & Award Subcontracts	3	3	11-Jan-21	13-Jan-21	Electrical Lighting-Bid & Award Subcontracts																	
P10800	Signage-Bid & Award Subcontracts	3	3	11-Jan-21	13-Jan-21	Signage-Bid & Award Subcontracts																	
P15500	HVAC-Bid & Award Subcontracts	3	3	11-Jan-21	13-Jan-21	HVAC-Bid & Award Subcontracts																	
P16020	Electrical Transformers-Bid & Award Subcontracts	3	3	14-Jan-21	18-Jan-21	Electrical Transformers-Bid & Award Subcontracts																	
P2900	Landscaping-Bid & Award Subcontracts	3	3	14-Jan-21	18-Jan-21	Landscaping-Bid & Award Subcontracts																	

■ Remaining Level of Effort ■ Critical Remaining Work
■ Actual Level of Effort ◆ Milestone
■ Actual Work — Summary
■ Remaining Work

McNair Park Project-15DEC20
Progress Thru: 15-Dec-20
File Name:MCN-15DEC20

Run Date: 15-Dec-20
Data Date: 15-Dec-20
Page 2 of 8



Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish	2020						2021												
						Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
P15000	Plumbing-Bid & Award Subcontracts	3	3	14-Jan-21	18-Jan-21								█ Plumbing-Bid & Award Subcontracts											
P10220	Shade Structures-Bid & Award Subcontracts	3	3	19-Jan-21	21-Jan-21								█ Shade Structures-Bid & Award Subcontracts											
P7300	Roofing-Bid & Award Subcontracts	3	3	19-Jan-21	21-Jan-21								█ Roofing-Bid & Award Subcontracts											
P9010	Ceiling-Bid & Award Subcontracts	3	3	22-Jan-21	26-Jan-21								█ Ceiling-Bid & Award Subcontracts											
P12020	Site Amenities-Bid & Award Subcontracts	3	3	27-Jan-21	29-Jan-21								█ Site Amenities-Bid & Award Subcontracts											
P10000	Division 10-Bid & Award Subcontracts	3	3	01-Feb-21	03-Feb-21								█ Division 10-Bid & Award Subcontracts											
P11000	Interior Exercise Equipment-Bid & Award Subcontracts	3	3	04-Feb-21	08-Feb-21								█ Interior Exercise Equipment-Bid & Award Subcontracts											
P11010	Exterior Exercise Equipment-Bid & Award Subcontracts	3	3	09-Feb-21	11-Feb-21								█ Exterior Exercise Equipment-Bid & Award Subcontracts											
P11400	Food Service-Bid & Award Subcontracts	3	3	12-Feb-21	16-Feb-21								█ Food Service-Bid & Award Subcontracts											
Prep & Submit Shops/Submittals (incl KL Rev)		58	58	17-Dec-20	11-Mar-21								█ Prep & Submit Shops/Submittals (incl KL Rev)											
S2200	Civil-Prep & Submit Shops/Submittals (incl KL Rev)	10	10	17-Dec-20	04-Jan-21								█ Civil-Prep & Submit Shops/Submittals (incl KL Rev)											
S2500	Paving/Striping-Prep & Submit Shops/Submittals (incl KL Rev)	10	10	21-Dec-20	06-Jan-21								█ Paving/Striping-Prep & Submit Shops/Submittals (incl KL Rev)											
S12000	Playground Shops-Prep & Submit Shops/Submittals (incl KL Rev)	15	15	28-Dec-20	18-Jan-21								█ Playground Shops-Prep & Submit Shops/Submittals (incl KL Rev)											
S7850	Laminate Panel Ceiling-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	21-Dec-20	20-Jan-21								█ Laminate Panel Ceiling-Prep & Submit Shops/Submittals (incl KL Rev)											
S6170	Millwork-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	21-Dec-20	20-Jan-21								█ Millwork-Prep & Submit Shops/Submittals (incl KL Rev)											
S2855	Picket Fence-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	21-Dec-20	20-Jan-21								█ Picket Fence-Prep & Submit Shops/Submittals (incl KL Rev)											
S11020	Basketball Hoops-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	21-Dec-20	20-Jan-21								█ Basketball Hoops-Prep & Submit Shops/Submittals (incl KL Rev)											
S8250	OH Door-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	21-Dec-20	20-Jan-21								█ OH Door-Prep & Submit Shops/Submittals (incl KL Rev)											
S8100	HM Doors-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	21-Dec-20	20-Jan-21								█ HM Doors-Prep & Submit Shops/Submittals (incl KL Rev)											
S8400	Storefront Shops-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	21-Dec-20	20-Jan-21								█ Storefront Shops-Prep & Submit Shops/Submittals (incl KL Rev)											
S2920	Bleacher/Field Goal-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	21-Dec-20	20-Jan-21								█ Bleacher/Field Goal-Prep & Submit Shops/Submittals (incl KL Rev)											
S2950	Press Box-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	21-Dec-20	20-Jan-21								█ Press Box-Prep & Submit Shops/Submittals (incl KL Rev)											
S16500	Field Lighting Shops-Prep & Submit Shops/Submittals (incl KL Rev)	10	10	11-Jan-21	22-Jan-21								█ Field Lighting Shops-Prep & Submit Shops/Submittals (incl KL Rev)											
S3000	Rebar Shops-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	28-Dec-20	25-Jan-21								█ Rebar Shops-Prep & Submit Shops/Submittals (incl KL Rev)											
S2930	Turf-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	28-Dec-20	25-Jan-21								█ Turf-Prep & Submit Shops/Submittals (incl KL Rev)											
S10800	Signage-Prep & Submit Shops/Submittals (incl KL Rev)	10	10	14-Jan-21	27-Jan-21								█ Signage-Prep & Submit Shops/Submittals (incl KL Rev)											
S9000	Exterior Metal Framing-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	31-Dec-20	28-Jan-21								█ Exterior Metal Framing-Prep & Submit Shops/Submittals (incl KL Rev)											
S15000	Plumbing-Prep & Submit Shops/Submittals (incl KL Rev)	10	10	19-Jan-21	01-Feb-21								█ Plumbing-Prep & Submit Shops/Submittals (incl KL Rev)											
S5000	Structural Steel Shops-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	06-Jan-21	02-Feb-21								█ Structural Steel Shops-Prep & Submit Shops/Submittals (incl KL Rev)											
S15500	HVAC-Prep & Submit Shops/Submittals (incl KL Rev)	15	15	14-Jan-21	03-Feb-21								█ HVAC-Prep & Submit Shops/Submittals (incl KL Rev)											
S16000	Electrical Switchgear-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	11-Jan-21	05-Feb-21								█ Electrical Switchgear-Prep & Submit Shops/Submittals (incl KL Rev)											
S2900	Landscaping-Prep & Submit Shops/Submittals (incl KL Rev)	15	15	19-Jan-21	08-Feb-21								█ Landscaping-Prep & Submit Shops/Submittals (incl KL Rev)											
S16010	Electrical Lighting-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	14-Jan-21	10-Feb-21								█ Electrical Lighting-Prep & Submit Shops/Submittals (incl KL Rev)											
S7300	Roofing Shops-Prep & Submit Shops/Submittals (incl KL Rev)	15	15	22-Jan-21	11-Feb-21								█ Roofing Shops-Prep & Submit Shops/Submittals (incl KL Rev)											
S16020	Electrical Transformers-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	19-Jan-21	15-Feb-21								█ Electrical Transformers-Prep & Submit Shops/Submittals (incl KL Rev)											
S10000	Division 10-Prep & Submit Shops/Submittals (incl KL Rev)	10	10	04-Feb-21	17-Feb-21								█ Division 10-Prep & Submit Shops/Submittals (incl KL Rev)											
S10220	Shade Structure Shops-Prep & Submit Shops/Submittals (incl KL Rev) (+D)	20	20	22-Jan-21	18-Feb-21								█ Shade Structure Shops-Prep & Submit Shops/Submittals (incl KL Rev) (+D)											
S11000	Interior Exercise Equipment-Prep & Submit Shops/Submittals (incl KL Rev)	10	10	09-Feb-21	22-Feb-21								█ Interior Exercise Equipment-Prep & Submit Shops/Submittals (incl KL Rev)											
S9010	Ceiling-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	27-Jan-21	23-Feb-21								█ Ceiling-Prep & Submit Shops/Submittals (incl KL Rev)											
S12020	Site Amenities-Prep & Submit Shops/Submittals (incl KL Rev)	20	20	01-Feb-21	26-Feb-21								█ Site Amenities-Prep & Submit Shops/Submittals (incl KL Rev)											
S11400	Food Service-Prep & Submit Shops/Submittals (incl KL Rev)	15	15	17-Feb-21	09-Mar-21								█ Food Service-Prep & Submit Shops/Submittals (incl KL Rev)											
S11010	Exterior Exercise Equipment-Prep & Submit Shops/Submittals (incl KL Rev) (+D)	20	20	12-Feb-21	11-Mar-21								█ Exterior Exercise Equipment-Prep & Submit Shops/Submittals (incl KL Rev) (+D)											
A/E Review & Apr Shops/Submittals		66	66	05-Jan-21	06-Apr-21								█ A/E Review & Apr Shops/Submittals											
SA2200	Civil-A/E Review & Apr Shops/Submittals	10	10	05-Jan-21	18-Jan-21								█ Civil-A/E Review & Apr Shops/Submittals											
SA2500	Paving/Striping-A/E Review & Apr Shops/Submittals	10	10	07-Jan-21	20-Jan-21								█ Paving/Striping-A/E Review & Apr Shops/Submittals											
SA10800	Signage-A/E Review & Apr Shops/Submittals	10	10	28-Jan-21	10-Feb-21								█ Signage-A/E Review & Apr Shops/Submittals											
SA12000	Playground Shops-A/E Review & Apr Shops/Submittals	20	20	19-Jan-21	15-Feb-21								█ Playground Shops-A/E Review & Apr Shops/Submittals											
SA2920	Bleacher/Field Goal-A/E Review & Apr Shops/Submittals	20	20	20-Jan-21	16-Feb-21								█ Bleacher/Field Goal-A/E Review & Apr Shops/Submittals											
SA2950	Press Box-A/E Review & Apr Shops/Submittals	20	20	20-Jan-21	16-Feb-21								█ Press Box-A/E Review & Apr Shops/Submittals											
SA7850	Laminate Panel Ceiling-A/E Review & Apr Shops/Submittals	20	20	21-Jan-21	17-Feb-21								█ Laminate Panel Ceiling-A/E Review & Apr Shops/Submittals											
SA6170	Millwork-A/E Review & Apr Shops/Submittals	20	20	21-Jan-21	17-Feb-21								█ Millwork-A/E Review & Apr Shops/Submittals											

█ Remaining Level of Effort █ Critical Remaining Work
█ Actual Level of Effort ◆ Milestone
█ Actual Work — Summary
█ Remaining Work

McNair Park Project-15DEC20
 Progress Thru: 15-Dec-20
 File Name:MCN-15DEC20

Run Date: 15-Dec-20
 Data Date: 15-Dec-20
 Page 3 of 8



Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish	2020												2021											
						Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec					
SA2855	Picket Fence-A/E Review & Apr Shops/Submittals	20	20	21-Jan-21	17-Feb-21											█	Picket Fence-A/E Review & Apr Shops/Submittals												
SA11020	Basketball Hoops-A/E Review & Apr Shops/Submittals	20	20	21-Jan-21	17-Feb-21											█	Basketball Hoops-A/E Review & Apr Shops/Submittals												
SA8250	OH Door-A/E Review & Apr Shops/Submittals	20	20	21-Jan-21	17-Feb-21											█	OH Door-A/E Review & Apr Shops/Submittals												
SA8100	HM Doors-A/E Review & Apr Shops/Submittals	20	20	21-Jan-21	17-Feb-21											█	HM Doors-A/E Review & Apr Shops/Submittals												
SA8400	Storefront Shops-A/E Review & Apr Shops/Submittals	20	20	21-Jan-21	17-Feb-21											█	Storefront Shops-A/E Review & Apr Shops/Submittals												
SA16500	Field Lighting Shops-A/E Review & Apr Shops/Submittals	20	20	25-Jan-21	19-Feb-21											█	Field Lighting Shops-A/E Review & Apr Shops/Submittals												
SA2930	Turf-A/E Review & Apr Shops/Submittals	20	20	25-Jan-21	19-Feb-21											█	Turf-A/E Review & Apr Shops/Submittals												
SA3000	Rebar Shops-A/E Review & Apr Shops/Submittals	20	20	26-Jan-21	22-Feb-21											█	Rebar Shops-A/E Review & Apr Shops/Submittals												
SA5000	Structural Steel Shops-A/E Review & Apr Shops/Submittals	15	15	03-Feb-21	23-Feb-21											█	Structural Steel Shops-A/E Review & Apr Shops/Submittals												
SA9000	Exterior Metal Framing-A/E Review & Apr Shops/Submittals	20	20	29-Jan-21	25-Feb-21											█	Exterior Metal Framing-A/E Review & Apr Shops/Submittals												
SA15000	Plumbing-A/E Review & Apr Shops/Submittals	20	20	02-Feb-21	01-Mar-21											█	Plumbing-A/E Review & Apr Shops/Submittals												
SA15500	HVAC-A/E Review & Apr Shops/Submittals	20	20	04-Feb-21	03-Mar-21											█	HVAC-A/E Review & Apr Shops/Submittals												
SA10000	Division 10-A/E Review & Apr Shops/Submittals	10	10	18-Feb-21	03-Mar-21											█	Division 10-A/E Review & Apr Shops/Submittals												
SA16000	Electrical Switchgear-A/E Review & Apr Shops/Submittals	20	20	08-Feb-21	05-Mar-21											█	Electrical Switchgear-A/E Review & Apr Shops/Submittals												
SA2900	Landscaping-A/E Review & Apr Shops/Submittals	20	20	09-Feb-21	08-Mar-21											█	Landscaping-A/E Review & Apr Shops/Submittals												
SA11000	Interior Exercise Equipment-A/E Review & Apr Shops/Submittals	10	10	23-Feb-21	08-Mar-21											█	Interior Exercise Equipment-A/E Review & Apr Shops/Submittals												
SA16010	Electrical Lighting-A/E Review & Apr Shops/Submittals	20	20	11-Feb-21	10-Mar-21											█	Electrical Lighting-A/E Review & Apr Shops/Submittals												
SA7300	Roofing Shops-A/E Review & Apr Shops/Submittals	20	20	12-Feb-21	11-Mar-21											█	Roofing Shops-A/E Review & Apr Shops/Submittals												
SA16020	Electrical Transformers-A/E Review & Apr Shops/Submittals	20	20	16-Feb-21	15-Mar-21											█	Electrical Transformers-A/E Review & Apr Shops/Submittals												
SA10220	Shade Structure Shops-A/E Review & Apr Shops/Submittals	20	20	19-Feb-21	18-Mar-21											█	Shade Structure Shops-A/E Review & Apr Shops/Submittals												
SA9010	Ceiling-A/E Review & Apr Shops/Submittals	20	20	24-Feb-21	23-Mar-21											█	Ceiling-A/E Review & Apr Shops/Submittals												
SA11010	Exterior Exercise Equipment-A/E Review & Apr Shops/Submittals	10	10	12-Mar-21	25-Mar-21											█	Exterior Exercise Equipment-A/E Review & Apr Shops/Submittals												
SA12020	Site Amenities-A/E Review & Apr Shops/Submittals	20	20	01-Mar-21	26-Mar-21											█	Site Amenities-A/E Review & Apr Shops/Submittals												
SA11400	Food Service-A/E Review & Apr Shops/Submittals	20	20	10-Mar-21	06-Apr-21											█	Food Service-A/E Review & Apr Shops/Submittals												
Fabricate & Deliver		160	160	14-Jan-21	27-Aug-21											█ Fabricate & Deliver													
D2500	Paving/Striping-Fabricate & Deliver	5	5	21-Jan-21	27-Jan-21											█	Paving/Striping-Fabricate & Deliver												
D2200	Civil-Fabricate & Deliver	15	15	19-Jan-21	08-Feb-21											█	Civil-Fabricate & Deliver												
D11020	Basketball Hoops-Fabricate & Deliver	5	5	18-Feb-21	24-Feb-21											█	Basketball Hoops-Fabricate & Deliver												
D5000	Anchor Bolts-Fabricate & Deliver	10	10	17-Feb-21	02-Mar-21											█	Anchor Bolts-Fabricate & Deliver												
D10800	Signage-Fabricate & Deliver	15	15	11-Feb-21	03-Mar-21											█	Signage-Fabricate & Deliver												
D9000	Exterior Metal Framing-Fabricate & Deliver	5	5	26-Feb-21	04-Mar-21											█	Exterior Metal Framing-Fabricate & Deliver												
D2925	Field Goal Posts-Fabricate & Deliver	20	20	17-Feb-21	16-Mar-21											█	Field Goal Posts-Fabricate & Deliver												
D15510	HVAC Ducts-Fabricate & Deliver	10	10	04-Mar-21	17-Mar-21											█	HVAC Ducts-Fabricate & Deliver												
D8100	HM Doors-Fabricate & Deliver	20	20	18-Feb-21	17-Mar-21											█	HM Doors-Fabricate & Deliver												
D2930	Turf-Fabricate & Deliver	20	20	22-Feb-21	19-Mar-21											█	Turf-Fabricate & Deliver												
D15500	AHU-Fabricate & Deliver	50	50	14-Jan-21	24-Mar-21											█	AHU-Fabricate & Deliver												
D15000	Plumbing-Fabricate & Deliver	20	20	02-Mar-21	29-Mar-21											█	Plumbing-Fabricate & Deliver												
D15010	Roof Drains-Fabricate & Deliver	20	20	02-Mar-21	29-Mar-21											█	Roof Drains-Fabricate & Deliver												
D5010	Roof Joists/Structural Steel-Fabricate & Deliver	25	25	24-Feb-21	30-Mar-21											█	Roof Joists/Structural Steel-Fabricate & Deliver												
D10000	Division 10-Fabricate & Deliver	20	20	04-Mar-21	31-Mar-21											█	Division 10-Fabricate & Deliver												
D8250	OH Door-Fabricate & Deliver	30	30	18-Feb-21	31-Mar-21											█	OH Door-Fabricate & Deliver												
D6170	Millwork-Fabricate & Deliver	30	30	18-Feb-21	31-Mar-21											█	Millwork-Fabricate & Deliver												
D7300	Roofing-Fabricate & Deliver	15	15	12-Mar-21	01-Apr-21											█	Roofing-Fabricate & Deliver												
D2900	Landscaping-Fabricate & Deliver	20	20	09-Mar-21	05-Apr-21											█	Landscaping-Fabricate & Deliver												
D15520	HVAC Exhaust Fans-Fabricate & Deliver	30	30	04-Mar-21	14-Apr-21											█	HVAC Exhaust Fans-Fabricate & Deliver												
D2855	Picket Fence-Fabricate & Deliver	40	40	18-Feb-21	14-Apr-21											█	Picket Fence-Fabricate & Deliver												
D16500	Field Lighting-Fabricate & Deliver (Musco)	40	40	22-Feb-21	16-Apr-21											█	Field Lighting-Fabricate & Deliver (Musco)												
D11010	Exterior Exercise Equipment-Fabricate & Deliver	20	20	26-Mar-21	22-Apr-21											█	Exterior Exercise Equipment-Fabricate & Deliver												
D9010	Ceiling-Fabricate & Deliver	30	30	24-Mar-21	04-May-21											█	Ceiling-Fabricate & Deliver												
D7850	Laminate Panel Ceiling-Fabricate & Deliver	55	55	18-Feb-21	05-May-21											█	Laminate Panel Ceiling-Fabricate & Deliver												
D16020	Electrical Transformers-Fabricate & Deliver	40	40	16-Mar-21	10-May-21											█	Electrical Transformers-Fabricate & Deliver												
D2920	Bleachers-Fabricate & Deliver	60	60	17-Feb-21	11-May-21											█	Bleachers-Fabricate & Deliver												
D10220	Shade Structures-Fabricate & Deliver	40	40	19-Mar-21	13-May-21											█	Shade Structures-Fabricate & Deliver												
D11400	Food Service Equipment-Fabricate & Deliver	30	30	07-Apr-21	18-May-21											█	Food Service Equipment-Fabricate & Deliver												


- █ Remaining Level of Effort
- █ Actual Level of Effort
- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone
- Summary

McNair Park Project-15DEC20
 Progress Thru: 15-Dec-20
 File Name:MCN-15DEC20

Run Date: 15-Dec-20
 Data Date: 15-Dec-20
 Page 4 of 8



Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish	2020						2021												
						Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
D16010	Electrical Lighting-Fabricate & Deliver	60	60	11-Mar-21	03-Jun-21																			
D11000	Interior Exercise Equipment-Fabricate & Deliver (+D)	65	65	09-Mar-21	08-Jun-21																			
D2950	Press Box-Fabricate & Deliver	80	80	17-Feb-21	09-Jun-21																			
D16510	Parking Lot Lighting-Fabricate & Deliver	80	80	22-Feb-21	14-Jun-21																			
D12020	Site Amenities-Fabricate & Deliver	60	60	29-Mar-21	21-Jun-21																			
D12000	Playground Equipment-Fabricate & Deliver (RD)	90	90	16-Feb-21	22-Jun-21																			
D16000	Electrical Switchgear-Fabricate & Deliver	80	80	08-Mar-21	28-Jun-21																			
D8400	Storefront-Fabricate & Deliver (Release driven by field measure of steel)	55	55	11-Jun-21	27-Aug-21																			
Construction		226	223	07-Dec-20A	01-Nov-21																			
Convenience Store		58	55	07-Dec-20A	05-Mar-21																			
CSP-S	Complete Store Purchase	1	0	07-Dec-20A	07-Dec-20A																			
UT-S	Unification of Title	15	15	16-Dec-20	08-Jan-21																			
2145-S	Asbestos Survey	15	15	18-Dec-20	12-Jan-21																			
2085-S	Move Out	36	29	08-Dec-20A	28-Jan-21																			
2155-S	Abatement	10	10	29-Jan-21	11-Feb-21																			
2620-S	Salvage/Cut/Cap/Freon	5	5	12-Feb-21	18-Feb-21																			
FPL-100	FP&L Disconnect	15	15	29-Jan-21	18-Feb-21																			
DPI-S	Demo Permit Issued	5	5	19-Feb-21	25-Feb-21																			
2060-S	Demo Convenience Store	6	6	26-Feb-21	05-Mar-21																			
1081 Convenience Store		13	13	26-Feb-21	16-Mar-21																			
2075-1081	Tree Removal	1	1	26-Feb-21	26-Feb-21																			
2065-1081	Clear and Demolish Site	3	3	26-Feb-21	02-Mar-21																			
2085-1081	Excavate Retention Area	2	2	08-Mar-21	09-Mar-21																			
2060-1081	North East Drainage	5	5	08-Mar-21	12-Mar-21																			
2095-1081	Sod North East Area	2	2	15-Mar-21	16-Mar-21																			
Foundations		27	27	15-Mar-21	20-Apr-21																			
2000-S	Building Pad	3	3	15-Mar-21	17-Mar-21																			
3000	FRP Footers	10	10	18-Mar-21	31-Mar-21																			
3010	Stem Wall	3	3	01-Apr-21	05-Apr-21																			
2100	Backfill Stem Wall	2	2	06-Apr-21	07-Apr-21																			
2610	Electrical UG/R/Backfill	5	5	08-Apr-21	14-Apr-21																			
2600	Plumbing UG/R/Backfill	5	5	08-Apr-21	14-Apr-21																			
3020	Prep Slab	3	3	15-Apr-21	19-Apr-21																			
3030	Pour/Finish Slab	1	1	20-Apr-21	20-Apr-21																			
Structure		39	39	21-Apr-21	15-Jun-21																			
5000	Steel Columns	2	2	21-Apr-21	22-Apr-21																			
4000	Masonry Walls	4	4	23-Apr-21	28-Apr-21																			
3040	FRP Conc. Columns	5	5	29-Apr-21	05-May-21																			
3050	FRP Tie Beams/Tie Columns/RB's	10	10	06-May-21	19-May-21																			
5010	Beams/Joist/Deck (Hold storefront fabrication)	15	15	20-May-21	10-Jun-21																			
7350	Roof Drains	3	3	11-Jun-21	15-Jun-21																			
Exterior/Envelope		65	65	11-Jun-21	13-Sep-21																			
8250	OH Door	3	3	11-Jun-21	15-Jun-21																			
8100	HM Doors & Hardware	4	4	11-Jun-21	16-Jun-21																			
9000	Structural Framing/Parapet/Sheathing/AWVB	15	15	11-Jun-21	01-Jul-21																			
16000	Electrical OH Rough - Deck	5	5	02-Jul-21	09-Jul-21																			
8500	Punched Windows	5	5	02-Jul-21	09-Jul-21																			

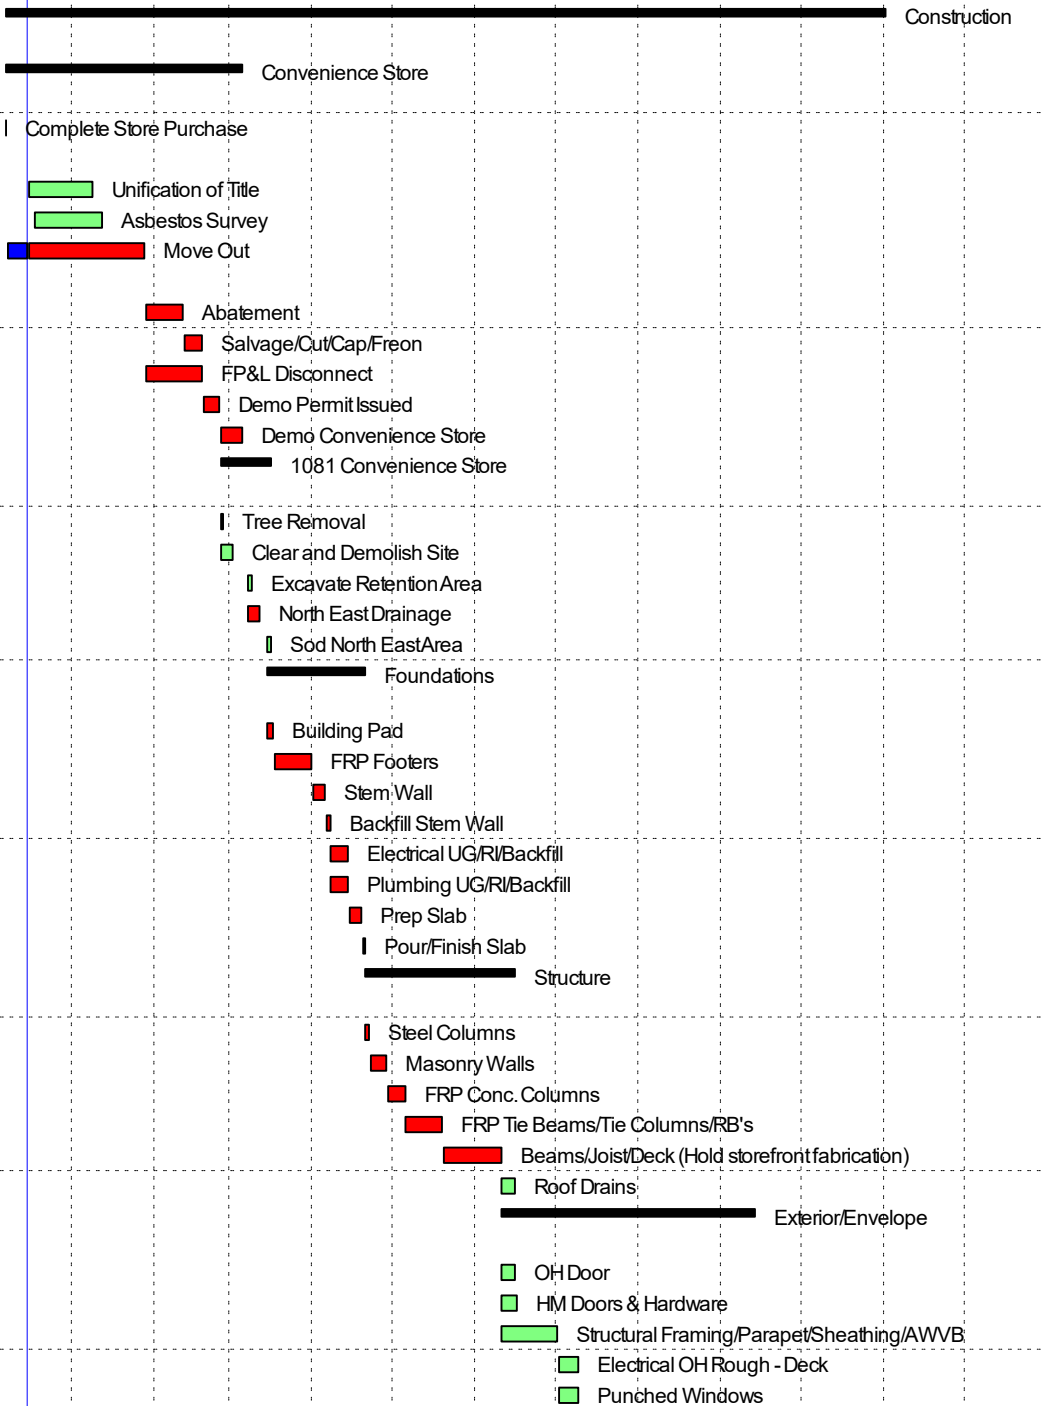


■ Remaining Level of Effort ■ Critical Remaining Work
■ Actual Level of Effort ◆ Milestone
■ Actual Work — Summary
■ Remaining Work

McNair Park Project-15DEC20
 Progress Thru: 15-Dec-20
 File Name:MCN-15DEC20

Run Date: 15-Dec-20
 Data Date: 15-Dec-20
 Page 5 of 8



Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish	2020						2021											
						Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
7300	Roof	8	8	02-Jul-21	14-Jul-21																		
6860	Laminate Panel Ceiling	5	5	12-Jul-21	16-Jul-21																		
9100	Stucco Walls/Parapet	13	13	12-Jul-21	28-Jul-21																		
9900	Paint Exterior	3	3	29-Jul-21	02-Aug-21																		
8400	Storefront	10	10	30-Aug-21	13-Sep-21																		
MEPF		7	7	25-Mar-21	02-Apr-21																		
15500	Install HVAC Equipment	3	3	25-Mar-21	29-Mar-21																		
16100	Electrical Connections for HVAC	4	4	30-Mar-21	02-Apr-21																		
Interiors		100	100	11-Jun-21	01-Nov-21																		
Rough-ins		79	79	11-Jun-21	01-Oct-21																		
9220	Hangers/Wall Z Clips	2	2	11-Jun-21	14-Jun-21																		
9020	Frame Walls/Rippers/Electrical One Side	12	12	15-Jul-21	30-Jul-21																		
16020	Floor/In Wall Electrical Rough	4	4	02-Aug-21	05-Aug-21																		
15020	In Wall Plumbing Rough	5	5	06-Aug-21	12-Aug-21																		
15030	In Wall Rough Inspection	1	1	13-Aug-21	13-Aug-21																		
15040	Plumbing OH RI	3	3	13-Aug-21	17-Aug-21																		
16030	Electrical OH RI	10	10	06-Aug-21	19-Aug-21																		
15510	HVAC/Duct/Insulation	5	5	14-Sep-21	20-Sep-21																		
9030	Frame Ceilings	6	6	21-Sep-21	28-Sep-21																		
16040	Finish MEP OH Rough	2	2	29-Sep-21	30-Sep-21																		
16050	OH Rough Inspection	1	1	01-Oct-21	01-Oct-21																		
Finishes		35	35	14-Sep-21	01-Nov-21																		
9040	Drywall/Finish Walls	5	5	14-Sep-21	20-Sep-21																		
9570	Polish Concrete/Epoxy Flooring	5	5	21-Sep-21	27-Sep-21																		
9560	Floor Tile	5	5	21-Sep-21	27-Sep-21																		
11480	Fitness Equipment	2	2	28-Sep-21	29-Sep-21																		
8410	Interior Storefront	3	3	28-Sep-21	30-Sep-21																		
9050	Drywall/Finish Ceilings	3	3	04-Oct-21	06-Oct-21																		
9060	Laminate Panel Ceiling	4	4	04-Oct-21	07-Oct-21																		
9910	Paint Walls & Ceiling	4	4	08-Oct-21	13-Oct-21																		
15520	HVAC Trim	3	3	14-Oct-21	18-Oct-21																		
11400	Food Service Equipment	2	2	18-Oct-21	19-Oct-21																		
6170	Install Millwork	4	4	14-Oct-21	19-Oct-21																		
16060	Electrical Trim	5	5	14-Oct-21	20-Oct-21																		
7310	Wall Tile	5	5	14-Oct-21	20-Oct-21																		
15050	Plumbing Trim	5	5	21-Oct-21	27-Oct-21																		
10000	Division 10	3	3	28-Oct-21	01-Nov-21																		
Electrical Room		21	21	02-Aug-21	30-Aug-21																		
16900	Install Transformers	10	10	02-Aug-21	13-Aug-21																		
16070	Install Switchgear	10	10	02-Aug-21	13-Aug-21																		
16080	Pull Homeruns	1	1	20-Aug-21	20-Aug-21																		
16090	Trim Out Panels	4	4	23-Aug-21	26-Aug-21																		
16910	FPL Checklist Complete	1	1	27-Aug-21	27-Aug-21																		
16920	Temp for Test Complete	1	1	30-Aug-21	30-Aug-21																		
Final Inspections		71	71	22-Jul-21	29-Oct-21																		
FI-2900	Final Landscaping	1	1	22-Jul-21	22-Jul-21																		
FE-2670	Final Engineering Inspection (Civil/Drainage)	1	1	23-Jul-21	23-Jul-21																		
FI-15500	Final HVAC	1	1	19-Oct-21	19-Oct-21																		
FI-16800	Final Fire	1	1	21-Oct-21	21-Oct-21																		
FI-16000	Final Electrical	1	1	21-Oct-21	21-Oct-21																		

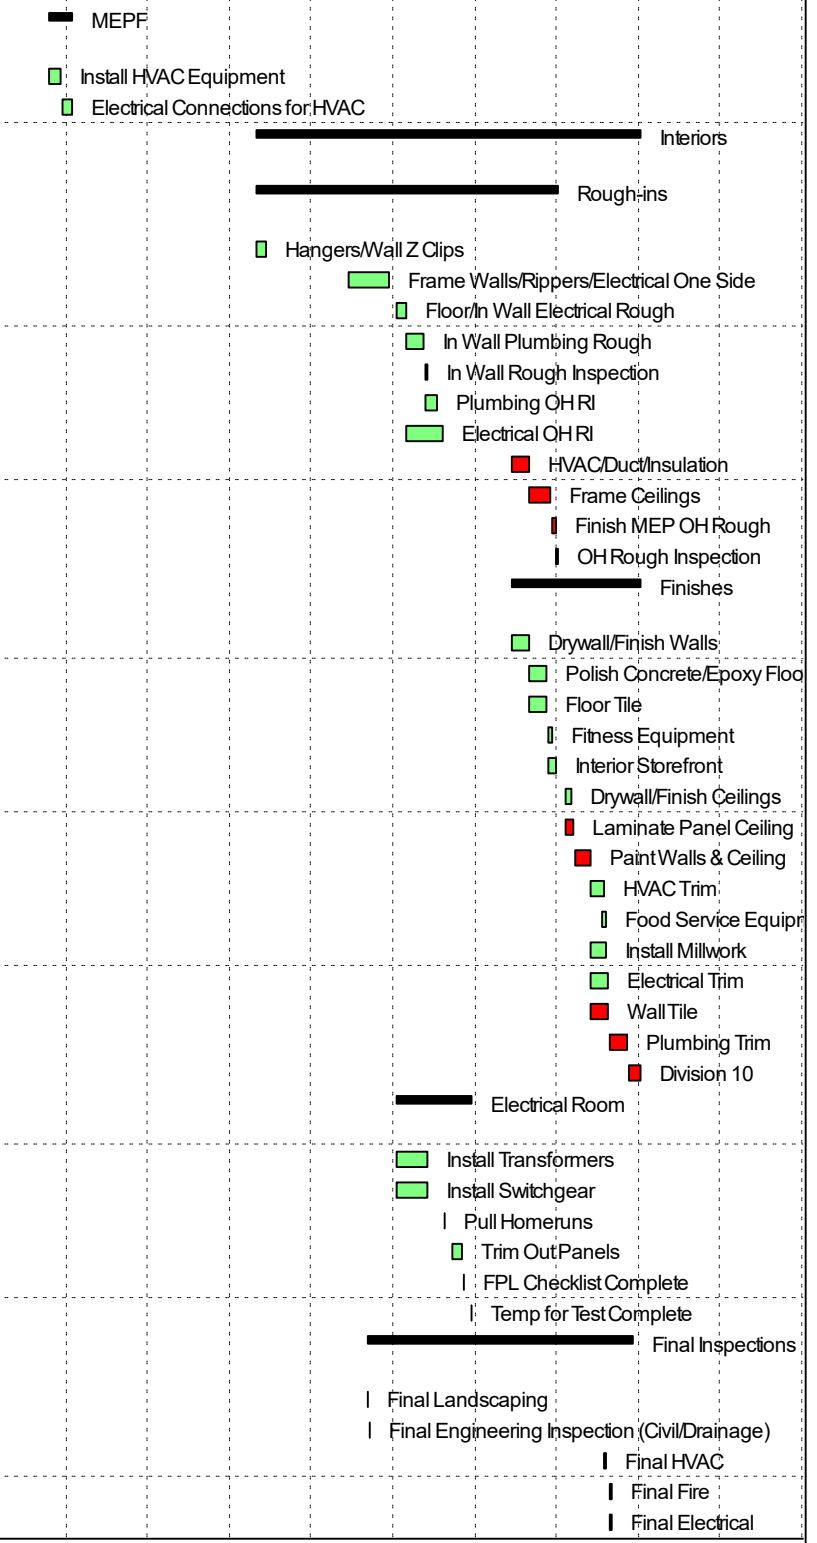

■ Remaining Level of Effort ■ Critical Remaining Work
■ Actual Level of Effort ◆ Milestone
■ Actual Work **█** Summary
■ Remaining Work

McNair Park Project-15DEC20
 Progress Thru: 15-Dec-20
 File Name:MCN-15DEC20

Run Date: 15-Dec-20
 Data Date: 15-Dec-20
 Page 6 of 8



Activity ID	Activity Name	Orig Dur	Rem Dur	Start	Finish	2020						2021											
						Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
2055-S	Resurface Basketball Courts	10	10	08-Jul-21	21-Jul-21																		
2870-S	Playground Fence	8	8	21-Jul-21	30-Jul-21																		



■ Remaining Level of Effort ■ Critical Remaining Work
■ Actual Level of Effort ◆ Milestone
■ Actual Work — Summary
■ Remaining Work

McNair Park Project-15DEC20
 Progress Thru: 15-Dec-20
 File Name:MCN-15DEC20

Run Date: 15-Dec-20
 Data Date: 15-Dec-20
 Page 8 of 8

