



North Pompano Park Improvements

#	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2021					2022	
							Q4	Q1	Q2	Q3	Q4	Q1	
1		North Pompano Park Improvements	286d	24-Aug-20	05-Oct-21	0d							05-Oct-21, North Pompano Park Im
2		Contract Dates (In Calendar Days)	256d	06-Oct-20	05-Oct-21	0d							05-Oct-21, Contract Dates (In Calend
3	A1870	NTP	0d	06-Oct-20*		0d							◆ NTP,06-Oct-20*
4	A1890	CONTRACT TIME (CALENDAR DAYS)	365d	06-Oct-20	05-Oct-21	0d							CONTRACT TIME (CALENDAR DAY
5	A1880	SUBSTANTIAL COMPLETION	0d		05-Oct-21	0d							◆ SUBSTANTIAL COMPLETION,
6		Submittals	30d	24-Aug-20	05-Oct-20	0d							05-Oct-20, Submittals
7	A2370	SUBMITTALS & SHOP DRAWINGS	30d	24-Aug-20	05-Oct-20	0d							SUBMITTALS & SHOP DRAWINGS
8		Construction - (In Standard 5- Day Work Days)	256d	06-Oct-20	05-Oct-21	0d							05-Oct-21, Construction - (In Stand
9		Staging Plan	15d	06-Oct-20	26-Oct-20	0d							26-Oct-20, Staging Plan
10	A1165	UTILITY LOCATES	2d	06-Oct-20	07-Oct-20	0d							UTILITY LOCATES
11	A1180	SURVEY-BOUNDARY LAYOUT	3d	08-Oct-20	12-Oct-20	0d							SURVEY-BOUNDARY LAYOUT
12	A1170	MOBILIZATION-STAGING & TEMP UTILITIES	5d	08-Oct-20	14-Oct-20	0d							MOBILIZATION-STAGING & TEMP UTILITIES
13	A1190	TEMP FENCE & SCREEN	3d	13-Oct-20	15-Oct-20	0d							TEMP FENCE & SCREEN
14	A1200	SILT FENCE & CATCH BASIN PROTECTION	3d	16-Oct-20	20-Oct-20	0d							SILT FENCE & CATCH BASIN PROTECTION
15	A1210	WASH OUT AREA	1d	21-Oct-20	21-Oct-20	0d							WASH OUT AREA
16	A1220	TREE PROTECTION	2d	22-Oct-20	23-Oct-20	0d							TREE PROTECTION
17	A1230	MOT SETUP	1d	26-Oct-20	26-Oct-20	0d							MOT SETUP
18		Demolition	32d	15-Oct-20	30-Nov-20	0d							30-Nov-20, Demolition
19	A1600	REMOVE EXISTING FENCING	5d	15-Oct-20	21-Oct-20	2d							REMOVE EXISTING FENCING
20	A1310	TREE REMOVALS AND RELOCATIONS	10d	26-Oct-20	06-Nov-20	0d							TREE REMOVALS AND RELOCATIONS
21	A1240	DEMOLITION OF EXISTING DUGOUT STRUCTURES	5d	09-Nov-20	13-Nov-20	0d							DEMOLITION OF EXISTING DUGOUT STRUTCURES
22	A1580	REMOVE & RELOCATE EXISTING SITE FURNISHINGS & EQUIPMENT	5d	09-Nov-20	13-Nov-20	0d							REMOVE & RELOCATE EXISTING SITE FURNISHINGS & EQUIPMENT
23	A1590	REMOVE EXISTING ASPHALT & CONCRETE PAVEMENT	10d	16-Nov-20	30-Nov-20	0d							REMOVE EXISTING ASPHALT & CONCRETE PAVEMENT
24		Site Preparation	58d	01-Dec-20	22-Feb-21	0d							22-Feb-21, Site Preparation
25	A1250	CLEAR & GRUB	10d	01-Dec-20	14-Dec-20	0d							CLEAR & GRUB
26	A1260	EXCAVATE/ROUGH GRADE SITE - REMOVE/STOCKPILE EXCESS	15d	01-Dec-20	21-Dec-20	0d							EXCAVATE/ROUGH GRADE SITE - REMOVE/STOCKPILE EXCESS
27	A1270	SITE UTILITIES - DRAINAGE/SEWER/WATER	24d	22-Dec-20	26-Jan-21	0d							SITE UTILITIES - DRAINAGE/SEWER/WATER
28	A1280	BACKFILL	5d	20-Jan-21	26-Jan-21	0d							BACKFILL
29	A1290	ELECTRICAL UNDERGROUND/SITE POWER	24d	20-Jan-21	22-Feb-21	0d							ELECTRICAL UNDERGROUND/SITE POWER
30	A1300	IRRIGATION ROUGHS	10d	09-Feb-21	22-Feb-21	0d							IRRIGATION ROUGHS
31		Restroom Building (Add Alternate)	59d	01-Dec-20	23-Feb-21	142d							23-Feb-21, Restroom Building (Add Alternate)

DATA DATE: 24-Aug-20
 ISSUE DATE: 25-Aug-20

North Pompano Park Improvements
 Page 1 of 3



West Architecture + Design, LLC
 West Construction, Inc


ALL CONSTRUCTION DURATIONS ARE IN WORK DAYS UNLESS OTHERWISE NOTED

NTP DATE: 24-Aug-20
 Final Completion Date: 05-Oct-21



North Pompano Park Improvements

#	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2021					2022	
							Q4	Q1	Q2	Q3	Q4	Q1	
32	A1860	SURVEY	2d	01-Dec-20	02-Dec-20	116d							
33	A1850	CLEAR & GRUB AREA	2d	03-Dec-20	04-Dec-20	116d							
34	A1350	LAYOUT PAD/PREP PAD	5d	05-Dec-20	09-Dec-20	116d							
35	A1380	FORM/REBAR & POUR FOOTERS	5d	10-Dec-20	14-Dec-20	116d							
36	A1410	CMU	10d	15-Dec-20	24-Dec-20	116d							
37	A1420	FORM/POUR TIE BEAM	3d	25-Dec-20	27-Dec-20	116d							
38	A1430	TRUSSES	2d	28-Dec-20	29-Dec-20	116d							
39	A1440	ROOFING	5d	30-Dec-20	03-Jan-21	116d							
40	A1450	HM FRAMES/DOORS/LOUVERS	3d	04-Jan-21	06-Jan-21	219d							
41	A1390	UG ROUGHS PLUMBING & ELECTRICAL	10d	04-Jan-21	13-Jan-21	202d							
42	A1400	FORM/REBAR & POUR SLAB	5d	14-Jan-21	18-Jan-21	202d							
43	A1480	HVAC ROUGH	5d	19-Jan-21	23-Jan-21	202d							
44	A1490	ELECTRICAL ROUGH	5d	19-Jan-21	23-Jan-21	202d							
45	A1500	PLUMBING ROUGH	5d	19-Jan-21	23-Jan-21	202d							
46	A1460	STUCCO WALL FINISH	7d	24-Jan-21	30-Jan-21	202d							
47	A1520	EPOXY PAINT	5d	31-Jan-21	04-Feb-21	202d							
48	A1550	STONE VENEER	5d	31-Jan-21	04-Feb-21	214d							
49	A1470	EXTERIOR PAINT	3d	05-Feb-21	07-Feb-21	214d							
50	A1560	PLUMBING/ELECTRICAL/MECH. FIXTURE & TRIMS	10d	05-Feb-21	14-Feb-21	202d							
51	A1570	TOILET ACCESSORIES AND PARTITIONS	5d	15-Feb-21	19-Feb-21	202d							
52	A1610	BUILDING SIGNS	2d	22-Feb-21	23-Feb-21	142d							
53	Soccer Fields		71d	27-Jan-21	05-May-21	91d							
54	A1990	REMOVE EXISTING SOD & EXCAVATE FIELD	15d	27-Jan-21	16-Feb-21	47d							
55	A2000	DRAINAGE PER PLANS	10d	17-Feb-21	02-Mar-21	47d							
56	A2010	IRRIGATION PER PLANS	10d	03-Mar-21	16-Mar-21	47d							
57	A2020	SUBGRADE FILL & COMPACT	10d	17-Mar-21	30-Mar-21	76d							
58	A2030	ADD FILL AS NECESSARY & FINAL GRADE	10d	31-Mar-21	13-Apr-21	76d							
59	A2350	INSTALL SPORTS LIGHTING	24d	31-Mar-21	03-May-21	91d							
60	A2040	INSTALL FIELD EQUIPMENT	5d	14-Apr-21	20-Apr-21	100d							
61	A2130	SOD FIELDS	10d	20-Apr-21	03-May-21	91d							
62	A2050	FIELD MARKINGS	2d	04-May-21	05-May-21	91d							
63	Football Field		71d	17-Feb-21	27-May-21	76d							

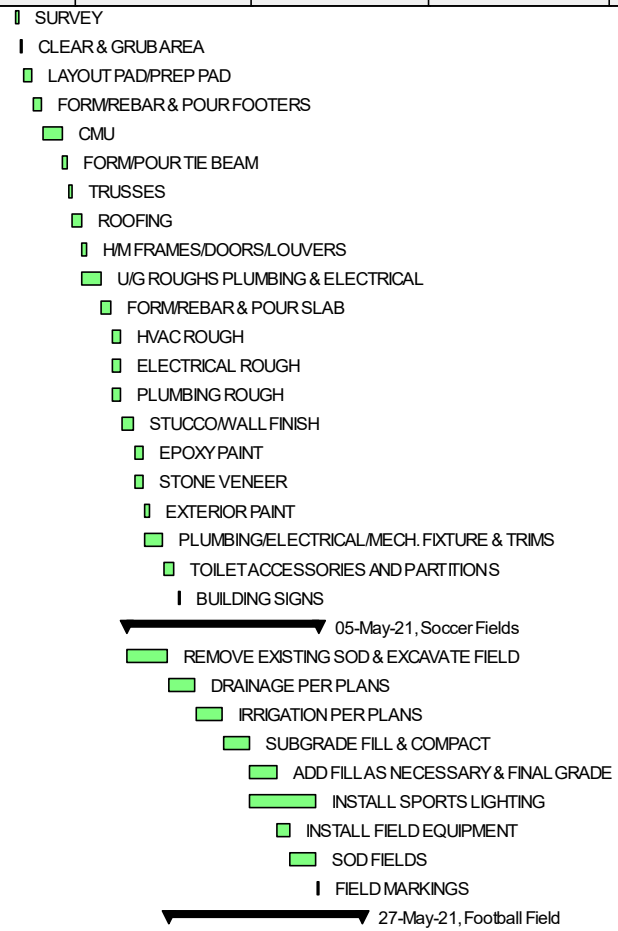

DATA DATE: 24-Aug-20
ISSUE DATE: 25-Aug-20

North Pompano Park Improvements
Page 2 of 3



West Architecture + Design, LLC
West Construction, Inc


ALL CONSTRUCTION DURATIONS ARE IN WORK DAYS UNLESS OTHERWISE NOTED

NTP DATE: 24-Aug-20
Final Completion Date: 05-Oct-21



North Pompano Park Improvements

#	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2021					2022	
							Q4	Q1	Q2	Q3	Q4	Q1	
64	A2060	REMOVE EXISTING SOD & EXCAVATE FIELD	10d	17-Feb-21	02-Mar-21	47d							
65	A2070	DRAINAGE PER PLANS	10d	03-Mar-21	16-Mar-21	47d							
66	A2080	IRRIGATION PER PLANS	10d	17-Mar-21	30-Mar-21	47d							
67	A2090	SUBGRADE FILL & COMPACT	5d	31-Mar-21	06-Apr-21	81d							
68	A2360	INSTALL SPORTS LIGHTING	24d	07-Apr-21	10-May-21	86d							
69	A2100	ADD FILL AS NECESSARY & FINAL GRADE	5d	14-Apr-21	20-Apr-21	76d							
70	A2110	INSTALL FIELD EQUIPMENT	5d	21-Apr-21	27-Apr-21	95d							
71	A2140	INSTALL ARTIFICIAL TURF	24d	21-Apr-21	25-May-21	76d							
72	A2120	FIELD MARKINGS	2d	26-May-21	27-May-21	76d							
73	Site Improvements		133d	23-Feb-21	30-Aug-21	0d							
74	A2150	INSTALL SUBGRADE & LIMEROCK	24d	23-Feb-21	26-Mar-21	0d							
75	A2160	INSTALL SITE LIGHTING	24d	23-Feb-21	26-Mar-21	0d							
76	A1340	INSTALL ASPHALT 1ST LIFT & TRAILS	24d	29-Mar-21	29-Apr-21	0d							
77	A1320	INSTALL CURBS	15d	30-Apr-21	20-May-21	0d							
78	A1330	INSTALL SIDEWALKS	10d	21-May-21	04-Jun-21	0d							
79	A1770	INSTALL IRRIGATION	15d	07-Jun-21	25-Jun-21	0d							
80	A1780	INSTALL TREES & SHRUBS	10d	28-Jun-21	12-Jul-21	0d							
81	A1810	INSTALL FENCING AND ACCESS CONTROLS	10d	13-Jul-21	26-Jul-21	0d							
82	A1820	INSTALL SOD	10d	27-Jul-21	09-Aug-21	0d							
83	A1830	INSTALL ASPHALT 2ND LIFT	5d	10-Aug-21	16-Aug-21	0d							
84	A1840	PARKING LOT STRIPING, SIGNS & BUMPERS	10d	17-Aug-21	30-Aug-21	0d							
85	A2170	INSTALL SITE FURNISHINGS	10d	17-Aug-21	30-Aug-21	0d							
86	Inspections		165d	15-Feb-21	05-Oct-21	0d							
87	A1900	FINAL ELECTRICAL INSPECTION	5d	15-Feb-21	19-Feb-21	144d							
88	A1910	FINAL PLUMBING INSPECTION	5d	15-Feb-21	19-Feb-21	144d							
89	A1920	FINAL MECHANICAL INSPECTION	5d	15-Feb-21	19-Feb-21	144d							
90	A1950	FINAL FIRE INSPECTION	5d	24-Feb-21	02-Mar-21	142d							
91	A1930	FINAL ZONING INSPECTION	5d	31-Aug-21	06-Sep-21	0d							
92	A1960	FINAL LANDSCAPING INSPECTION	5d	07-Sep-21	13-Sep-21	0d							
93	A1940	FINAL ENGINEERING INSPECTION	5d	14-Sep-21	20-Sep-21	0d							
94	A1970	FINAL BUILDING INSPECTION	5d	21-Sep-21	27-Sep-21	0d							
95	A1980	CO PROCESS	6d	28-Sep-21	05-Oct-21	0d							

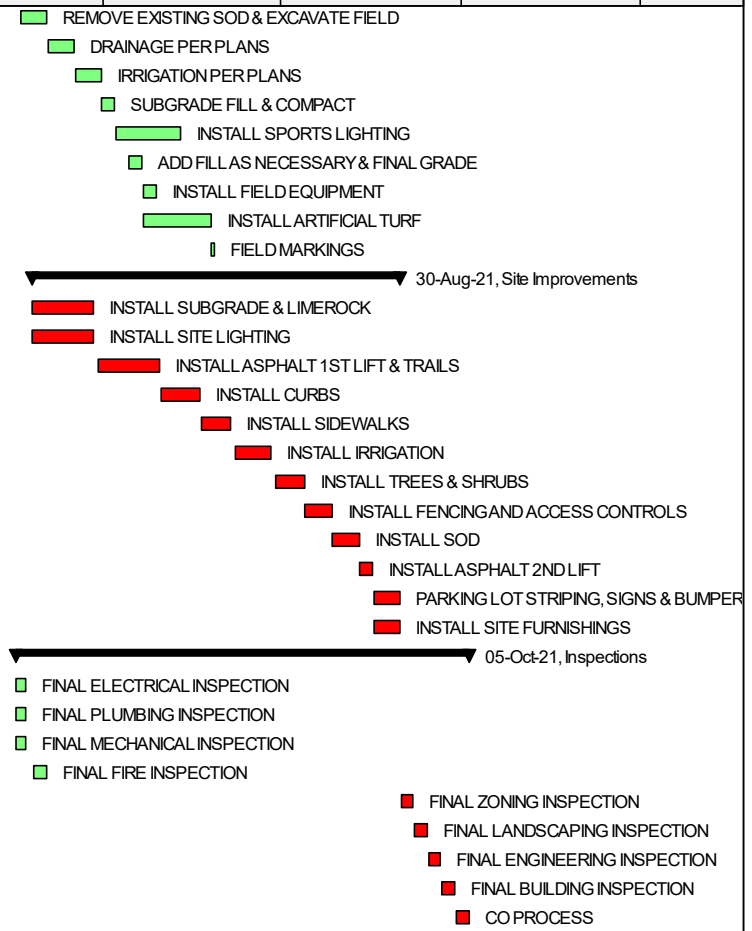

DATA DATE: 24-Aug-20
ISSUE DATE: 25-Aug-20

North Pompano Park Improvements
Page 3 of 3



West Architecture + Design, LLC
West Construction, Inc

ALL CONSTRUCTION DURATIONS ARE IN WORK DAYS UNLESS OTHERWISE NOTED

NTP DATE: 24-Aug-20
Final Completion Date: 05-Oct-21
