

November-December 2022 Project Dashboard

Project 19357 McNab Rd and Bridge Improvements

Prime Consultant:

Kimley»Horn

CMAR:

BURKHARDT
CONSTRUCTION, INC.

City of Pompano Beach

GO BOND DIRECTOR: FERNAND THONY, PE

PROJECT MANAGER: FERNAND THONY, PE

CURRENT PHASE: Schematics /Construction Docs

DESIGN TEAM: KIMLEY HORN

CONSTRUCTION TEAM: BURKHARDT

APPROVED BUDGET: \$19,500,000.00

PROJECT OBJECTIVES

The project main objectives include replacing the existing functionally obsolete bridge over C-14 on McNab Road and beautifying McNab Road corridor between Federal Highway and South Cypress Creek Road. The project will modernize the area by laying new paving, related drainage improvements, ADA sidewalks, street and pedestrian lighting, landscaping, bus shelters/benches and street furnishings.

PROJECT UPDATES

Staff met with residents of Cypress Landings and Cypress Club. The former submitted a series of comments to be addressed by legal. The latter unanimously approved the City's initiative. Legal staff is finalizing all agreements. A GMP is expected in January 2023.

PROJECT SCHEDULE MILESTONES


*** Schedule has been extended due to bridge scope change

DESIGN PHASE: Begins May 2019 Ends: July 2021
There are 5 phases before starting construction.

1. Concept Phase
2. Schematic Phase (Bridge)
3. Design Development Phase
4. Construction Documents (Roadway)
5. Permitting for Construction

CONSTRUCTION PHASE: Start date: (Varied) End date: **31-Aug-24**

PROJECT SITE LOCATION

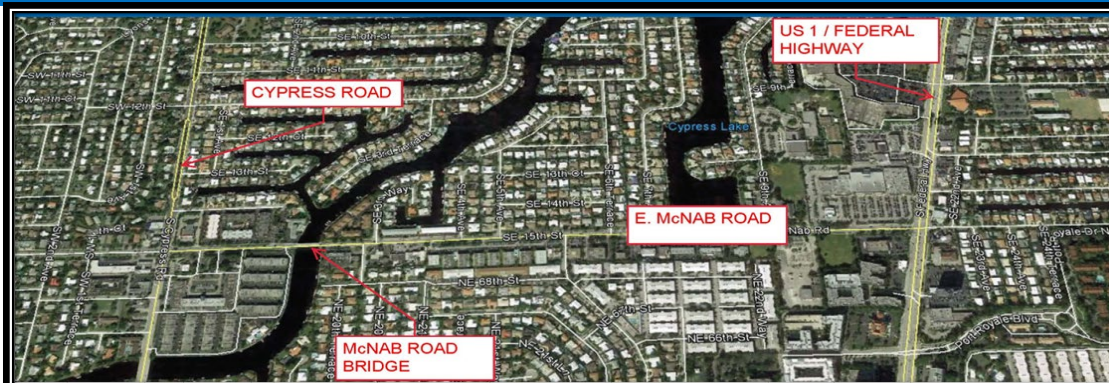

PROJECT PHOTOS

