



September - December 2023 Project Dashboard

Project 19377 Ocean Rescue Headquarters and Lifeguard Stations

Design Build:



City of Pompano Beach

GO BOND DIRECTOR: FERNAND THONY

PROJECT MANAGER: FERNAND THONY


CURRENT PHASE: CONSTRUCTION

DESIGN TEAM: WEST

CONSTRUCTION TEAM: WEST

APPROVED BUDGET: \$2,950,009.00

CONSTRUCTION PHOTOS

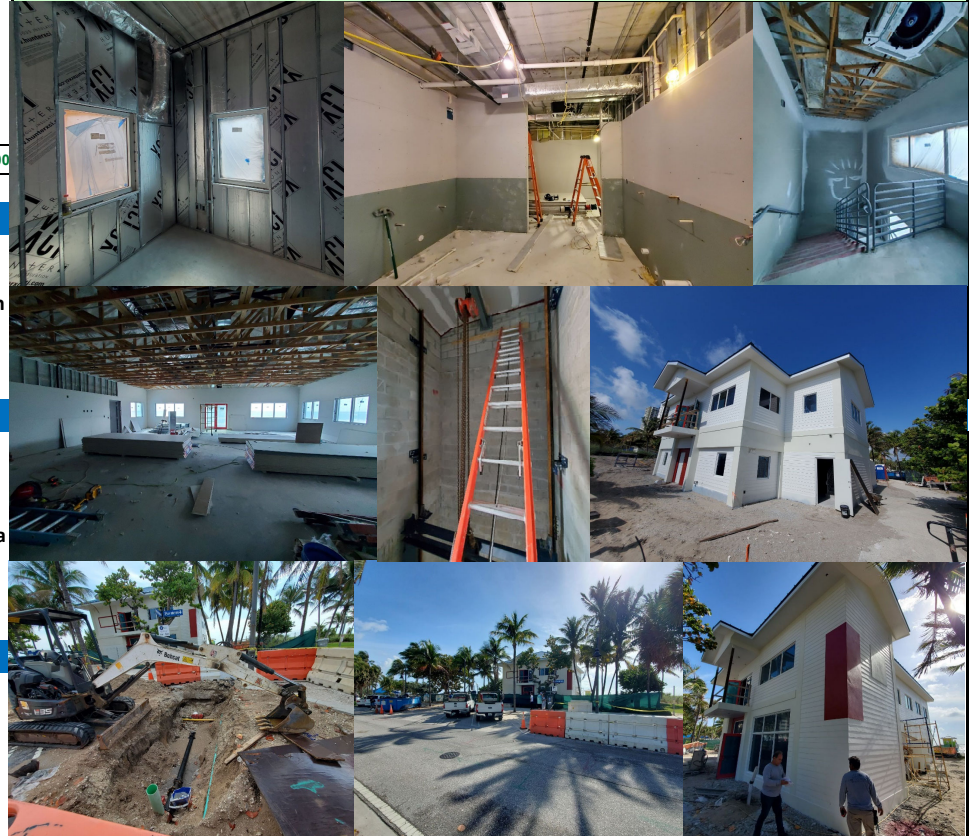

PROJECT OBJECTIVES

Create a new and modern facility for the Ocean Rescue Team and headquarters. Create a large conference room on the second floor.

PROJECT UPDATES

Project is nearly complete. All inspections have passed except Landscape Final and Zoning Final. No remaining issues to resolve. The new windows facing eastward are done. Furniture has been ordered. Project will receive a Certificate of Occupancy late January, early February 2024.

PROJECT SCHEDULE MILESTONES

DESIGN PHASE: Begins May 2019 Ends: Sept 2021

CONSTRUCTION PHASE:

Start date March 2022- End date February 2024

Substantial Completion anticipated September 2023

PROJECT LOCATION



PROJECT RENDERINGS

