



## June-July 2022 Project Dashboard

### Project 19373 New Fire Station 114

#### Design Build:

#### City of Pompano Beach



GO BOND DIRECTOR: FERNAND THONY, PE

PROJECT MANAGER: ARTHUR CANTERO, PE

CURRENT PHASE: CONSTRUCTION

DESIGN TEAM: DI POMPEO

CONSTRUCTION TEAM: DI POMPEO

APPROVED BUDGET: **\$5,750,000.00**

#### CONSTRUCTION PROGRESS




#### PROJECT OBJECTIVES

Construct a new fire station to be located at the corner of SW 36th Avenue and McNab Road to reduce response time and enhance fire and emergency services to the area which will include land acquisition and a new 2-story, multi-bay building.

#### PROJECT UPDATES

Interior finishes were completed including painting, flooring, restroom tile work and millwork  
Apparatus bay equipment and power cord installed  
Concrete driveways and parking areas all completed  
Plumbing fixtures installation completed  
Electrical wiring, interior and exterior lighting completed  
Elevator and fire alarm system installation in progress  
Project schedule has been delayed by 4-6 weeks due to material shortages and market scarcity

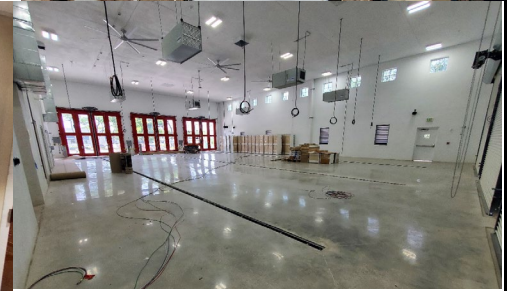

#### PROJECT SCHEDULE MILESTONES

DESIGN PHASE: May 2019-Aug 2020

There are 5 phases before construction:

1. Concept Phase
2. Schematic Phase
3. Design Development Phase
4. Construction Documents
5. Permitting for Construction

CONSTRUCTION PHASE: Feb 2021 - October 2023

