

Project 19368 North Pompano Park Improvements

Prime Consultant:



CMAR:



City of Pompano Beach

GO BOND DIRECTOR: HORACIO DANOVIH

PROJECT MANAGER: FERNAND THONY, PE

CURRENT PHASE: CONSTRUCTION

DESIGN TEAM: KEITH

CONSTRUCTION TEAM: WEST CONSTRUCTION

APPROVED BUDGET: \$3,885,163

CONSTRUCTION PROGRESS



PROJECT OBJECTIVES

This project includes renovation of the existing park facility to include upgraded and new lighted synthetic rectangular fields (soccer, football and baseball), expanded parking areas, concessions, new passive recreational areas, such as picnic lawn, new landscaping, access control, pedestrian paths.

PROJECT UPDATES

- Contractor crews have continued working onsite and most of the site work has been completed
- Currently working on the completion phase of this project

PROJECT SCHEDULE MILESTONES


DESIGN PHASE: Begins May 2019 Ends: November 2020

There are 5 phases before starting construction.

1. Concept Phase
2. Schematic Phase
3. Design Development Phase
4. Construction Documents
5. Construction Permitting

CONSTRUCTION PHASE: Start date April 2021- End date 30 July 2022

PROJECT SITE LOCATION

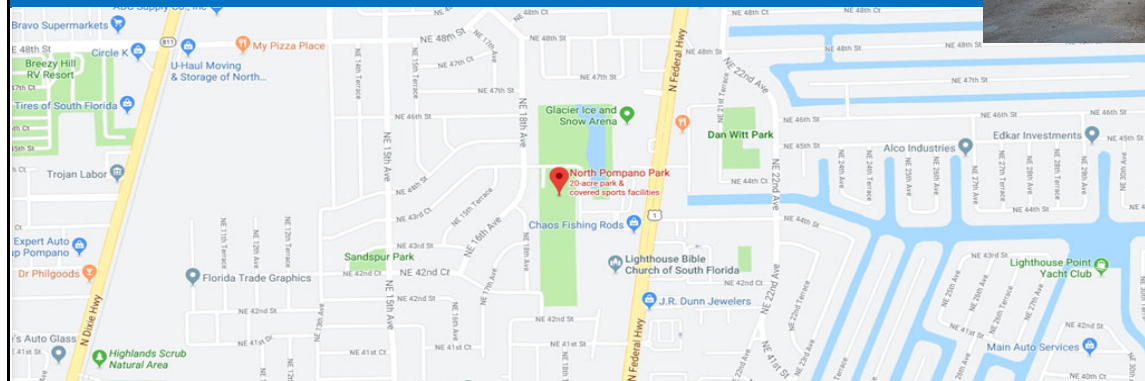

LEGEND

1. EXISTING STRUCTURE
2. DOG PARK
3. EXISTING PARKING
4. ADDITIONAL PARKING
5. MAIN ENTRANCE
6. SECONDARY ENTRANCE
7. MULTI-PURPOSE RECTANGULAR FIELD
8. BLEACHERS
9. FLEXIBLE OPEN SPACE
10. EXISTING PLAYGROUND
11. PICNIC AREA
12. PEDESTRIAN PATH
