

Project 19357 McNab Rd and Bridge Improvements

**Prime Consultant:**

**Kimley»Horn**

**CMAR:**

**BURKHARDT  
CONSTRUCTION, INC.**

**City of Pompano Beach**

**GO BOND DIRECTOR: FERNAND THONY, PE**

**PROJECT MANAGER: FERNAND THONY, PE**


**CURRENT PHASE: Schematics /Construction Docs**

**DESIGN TEAM: KIMLEY HORN**

**CONSTRUCTION TEAM: BURKHARDT**

**APPROVED BUDGET: \$19,500,000.00**

**PROJECT PHOTOS**

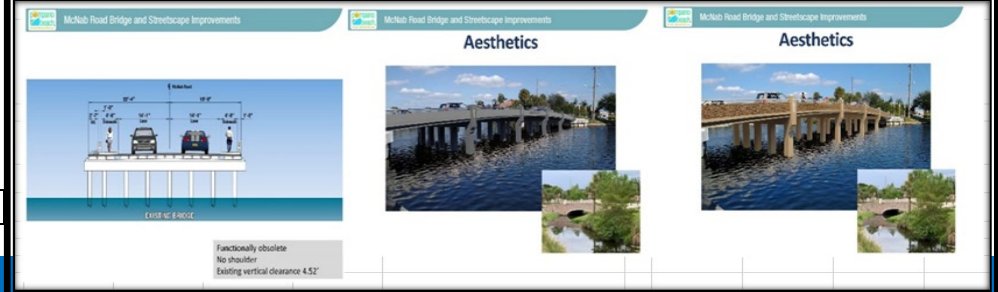

**PROJECT OBJECTIVES**

The project main objectives include replacing the existing functionally obsolete bridge over C-14 on McNab Road and beautifying McNab Road corridor between Federal Highway and South Cypress Creek Road. The project will modernize the area by laying new paving, related drainage improvements, ADA sidewalks, street and pedestrian lighting, landscaping, bus shelters/benches and street furnishings.

**PROJECT UPDATES**

The design team has finalized plans for City review and approval to modify the entrance to Cypress Club and the access driveway to Brewfish. Plans that were sent to South Florida Water Management District, Broward County, US Corps of Engineers and the Coast Guard for various approvals have yet to be returned with or without comments. Staff is waiting for 75% cost estimates from the CMAR.


**PROJECT SCHEDULE MILESTONES**

**\*\*\* Schedule has been extended due to bridge scope change**

**DESIGN PHASE:** Begins May 2019 Ends: July 2021  
There are 5 phases before starting construction.

1. Concept Phase
2. Schematic Phase (Bridge)
3. Design Development Phase
4. Construction Documents (Roadway)
5. Permitting for Construction

**CONSTRUCTION PHASE:** Start date: (Varied) End date: **31-Aug-24**

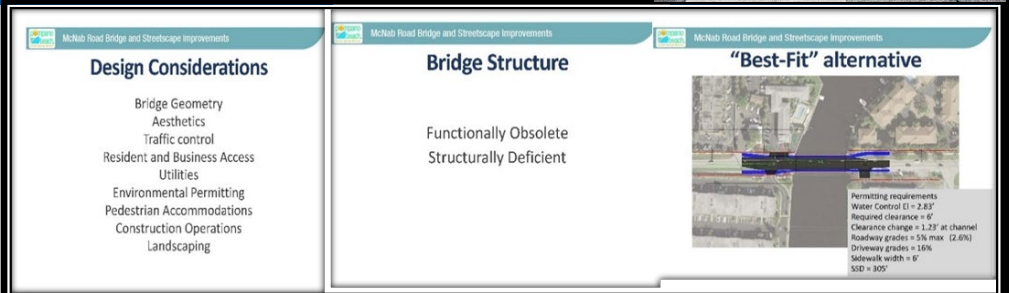

**PROJECT SITE LOCATION**

