



## October Project Dashboard

### Project 19358 Palm Aire Neighborhood Improvements

#### Prime Consultant:



#### CMAR:



#### City of Pompano Beach

GO BOND DIRECTOR: FERNAND THONY, PE

PROJECT MANAGER: FERNAND THONY, PE

CURRENT PHASE: SCHEMATICS & CONSTRUCTION DOCS

DESIGN TEAM: T.Y. LIN

CONSTRUCTION TEAM: WHITING TURNER

APPROVED BUDGET: \$3,891,316.00

#### EXISTING

##### Existing condition of both bridges

N. Palm Aire Drive Bridge (North)

- No Structural deficiencies listed in bridge inspection report.
- Railings are not crash worthy.

- Sidewalks are too narrow.
- No pedestrian lighting.



#### PROJECT OBJECTIVES

Improvements for two bridges spanning the C-14 Cypress Creek Canal: The N Palm Aire Dr bridge from Oaks Dr intersection to S Palm Aire Dr intersection, and the W Palm Aire Dr bridge (nearest the Herb Skolnick Center). Improvements include new pedestrian lighting, landscaping, and widened sidewalks. There will also be a new pedestrian trail, extending along the canal west side (adjacent to Oaks drive ) and east side (N Palm Aire Dr).

#### PROJECT UPDATES

2 North end walls at South Bridge ( Palm Aire Dr West) rebar installation completed

Pull test performed at doweled connections and successful

Partial electrical rough inspection approved

Structural inspection approved and formwork completed

Safety guardrail installation started and in progress


All MOT, silt fencing and turbidity barriers in place . Coordination with EOR for new lighting and power outlet at existing gazebo ongoing

Note: Project still on schedule except for minor delay in utilities coordination (FPL, Crown castle).

#### PROJECT SCHEDULE MILESTONES

DESIGN PHASE:	Begins May 2019	Ends: July 2021
CONSTRUCTION PHASE:	Start date May 2022	Ends: January 2023 - South Bridge
	Start date Feb 2023	Ends: January 2024 - North Bridge

#### PROJECT SCHEDULE MILESTONES AND LOCATION

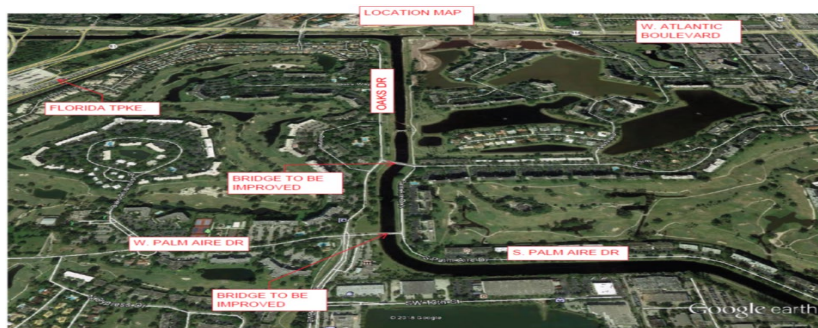

#### PROJECT PROGRESS PHOTOS

