



October 2022 Project Dashboard

Project 19373 New Fire Station 114

Design Build:

City of Pompano Beach

CONSTRUCTION PROGRESS



GO BOND DIRECTOR: FERNAND THONY, PE

PROJECT MANAGER: ARTHUR CANTERO, PE

CURRENT PHASE: CONSTRUCTION

DESIGN TEAM: DI POMPEO

CONSTRUCTION TEAM: DI POMPEO

APPROVED BUDGET: **\$5,750,000.00**




PROJECT OBJECTIVES

Construct a new fire station to be located at the corner of SW 36th Avenue and McNab Road to reduce response time and enhance fire and emergency services to the area which will include land acquisition and a new 2-story, multi-bay building.

PROJECT UPDATES

Project is substantially complete. Final inspections continue. Completion should be by the end of October or early November.

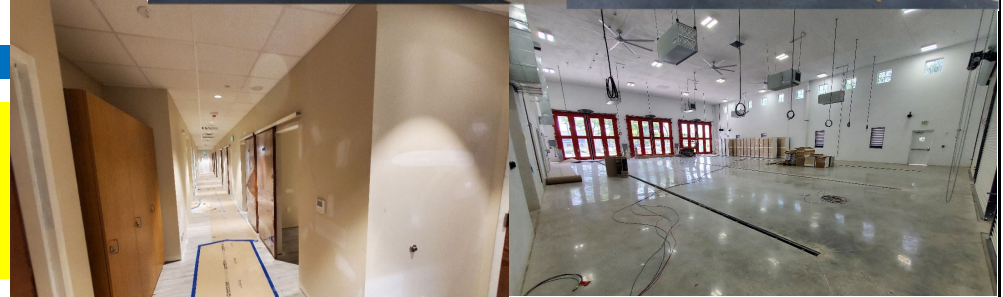

PROJECT SCHEDULE MILESTONES

DESIGN PHASE: May 2019-Aug 2020

There are 5 phases before construction:

1. Concept Phase
2. Schematic Phase
3. Design Development Phase
4. Construction Documents
5. Permitting for Construction

CONSTRUCTION PHASE: Feb 2021- October 2023

