



August/September 2022 Project Dashboard

Project 19367 Mitchell Moore Park Improvements

Prime Consultant:



CMAR:



City of Pompano Beach

GO BOND DIRECTOR: HORACIO DANOVIH

PROJECT MANAGER: FERNAND THONY, PE

CURRENT PHASE: CONSTRUCTION

DESIGN TEAM: WALTERS- ZACKRIA ARCHITECTS

CONSTRUCTION TEAM: SHIFF CONSTRUCTION

APPROVED BUDGET: **\$2,831,880**

CONSTRUCTION PROGRESS




PROJECT OBJECTIVES

Upgrades to this facility built in 1991 will include replacement of a grass field with synthetic (field turf), a new scoreboard, new fencing, a walking path, and shade structures over the bleacher area.

PROJECT UPDATES

Project is substantially complete pending delivery and installation of the Press Box by the Orange Bowl Committee. For now, the Orange Bowl improvement are scheduled to be completed in early December 2022. No new progress.

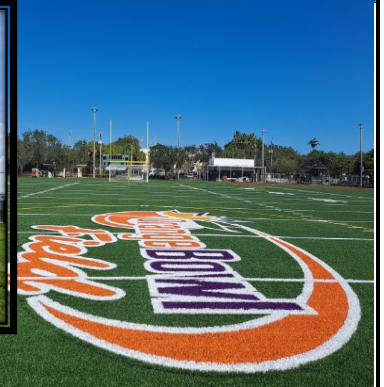

PROJECT SCHEDULE NOTES

DESIGN PHASE: Begins May 2019 Ends: January 2021

CONSTRUCTION PHASE Start date: February 2021- End date June 2022 (substantial completion)
CCTV camera installation and construction of the new walking pathway were completed during July 2022



PROJECT SITE LOCATION

