

October-November 2025 - Project Dashboard

Project 19357 McNab Rd and Bridge Improvements

Prime Consultant:

Kimley»Horn

General Contractor



City of Pompano Beach

GO BOND DIRECTOR: FERNAND THONY, PE

PROJECT MANAGER: FERNAND THONY, PE

CURRENT PHASE: CONSTRUCTION

DESIGN TEAM: KIMLEY HORN

CONSTRUCTION TEAM: H&A

GO BOND BUDGET: **\$16,500,000.00**

APPROVED CONTRACT **\$22,936,498.77**

PROJECT PHOTOS (CONSTRUCTION IN PROGRESS)



PROJECT OBJECTIVES

The project main objectives include replacing the existing functionally obsolete bridge over C-14 on McNab Road and beautifying McNab Road corridor between Federal Highway and South Cypress Creek Road. The project will modernize the area by laying new paving, related drainage improvements, ADA sidewalks, street and pedestrian lighting, landscaping, bus shelters/benches and street furnishings.

PROJECT UPDATES

Since its construction start date on July 14, the McNab Road Improvements project has been progressing steadily. Site clearing and selective tree removal have been completed. Crews started excavation and installation of the stormwater system which is still ongoing. The work is moving from Federal Highway westward to North Cypress Road. Approximately 80% of the proposed piping and structures in the south right of way has been completed. Additionally, the flatwork contractor has also placed nearly 70 % of new concrete curbing and sidewalks along the same right of way. Installation of the first of 2 utility crossings under the C-14 canal is in progress and scheduled to end by mid-December. Furthermore, initial work at one of 3- off site locations has started, namely the Cypress Club entrance relocation at the south-west corner of the existing bridge. Finally, a comprehensive traffic management plan has been implemented to minimize construction impacts including an engaged outreach process with the Community including nearby McNab Elementary to address potential concerns.


PROJECT SCHEDULE & MILESTONES

CONSTRUCTION:

STREETSCAPE (including, flatwork, stormwater, utilities ,etc) Start: July 2025 End: December 2026

BRIDGE (including demolition, piles and deck installation...) Start: May 2026 End: September 2026

CONCEPTUAL GRAPHICS

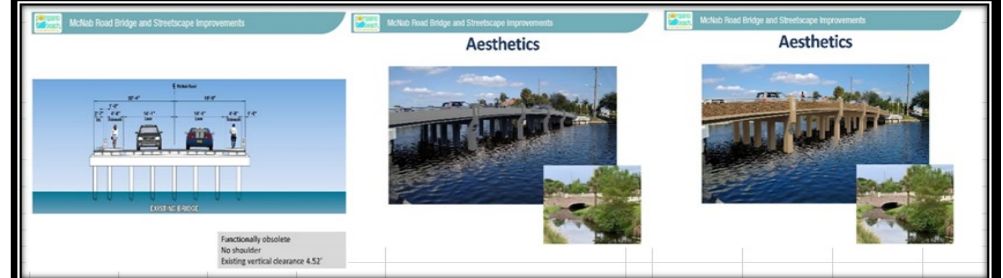

PROJECT SITE (LOCATION MAP)

