




Project and Phasing Schedule

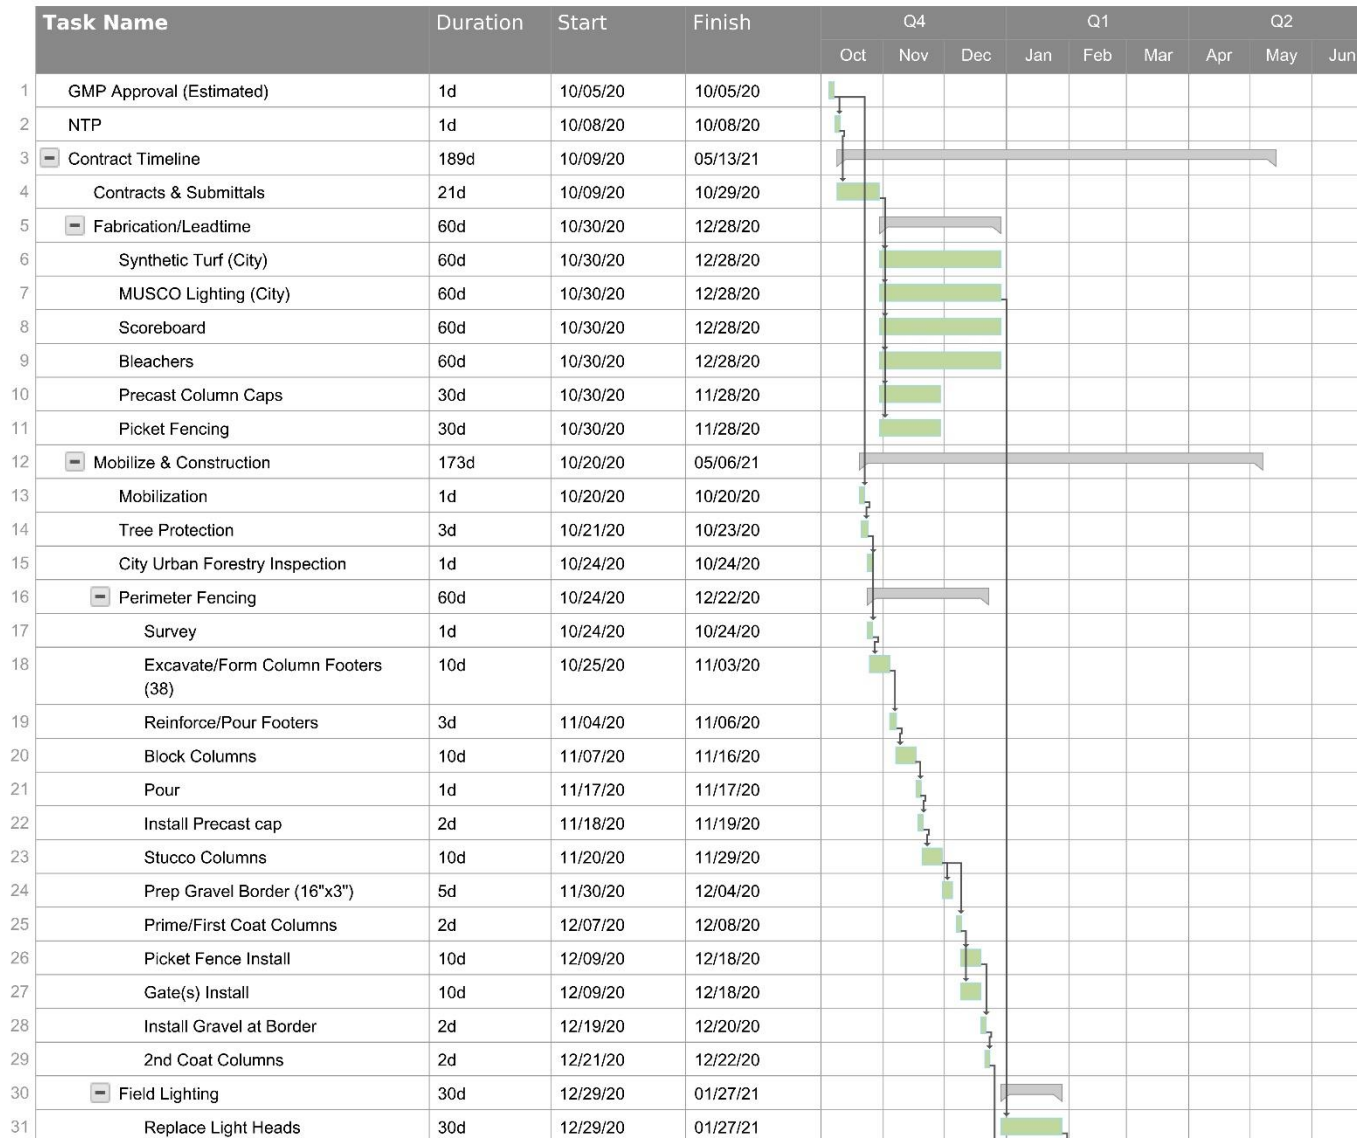

Project and Phasing Schedule

	Task Name	Duration	Start	Finish	Q4			Q1			Q2		
					Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
32	 Synthetic Field	73d	01/28/21	05/06/21									
33	Erosion Control	3d	01/28/21	01/30/21									
34	Excavate/Haul Exist. Subgrade	10d	01/31/21	02/11/21									
35	Prep/Base Install	10d	02/12/21	02/25/21									
36	Dewatering	7d	02/26/21	03/08/21									
37	Field/Exfiltration Drainage Install	21d	03/09/21	04/06/21									
38	Warning Track Install	7d	04/07/21	04/15/21									
39	Synthetic Turf Install	5d	04/16/21	04/22/21									
40	Baseline Fencing Install	10d	04/23/21	05/06/21									
41	 Sitework	28d	12/23/20	01/19/21									
42	Sidewalk Section (1,100 SF)	7d	12/23/20	12/29/20									
43	Remove/Install New Scoreboard	21d	12/30/20	01/19/21									
44	Final Inspections	5d	05/07/21	05/13/21									
45													
46													
47													
48													
