

### Prime Consultant:



### CMAR:



### City of Pompano Beach

GO BOND DIRECTOR: FERNAND THONY, PE

PROJECT MANAGER: FERNAND THONY, PE

CURRENT PHASE: CONSTRUCTION

DESIGN TEAM: KEITH

CONSTRUCTION TEAM: BURKHARDT

APPROVED BUDGET: **\$19,925,294.55**

### CONSTRUCTION PROGRESS



### PROJECT OBJECTIVES

The SR A1A Streetscape project involves various improvements from Hillsboro Inlet to Sunset Lane (South of Terra Mar Drive) such as undergrounding overhead utilities to reduce power outages during storms and improve the aesthetics of the corridor. Additional improvements include new sidewalks, bike lanes, traffic calming features, roadway resurfacing, lighting and landscaping. The Project will be broken into 2 Phase 1 - Phase 1 will address the roadway segment South of Atlantic Blvd while Phase 2 will encompass the roadway north of Atlantic Blvd.

### PROJECT UPDATES

Overhead Utilities Conversion Project Activities: November & December construction work progressed as per below:  
 11/1/22 - 11/4/22 MOT has now been extended beyond NE 14th St. The second span of MOT is setup now between N\$ 14th St and canal Drive. street. Crews are pulling cabled through installed conduits and recording logs information  
 11/7/22 - 11/11/22 Contractor crews are now proceeding with borings between 9th and 13th streets. Signalization crews working on trenching at the Sr A1A Atlantic Blvd. intersection and new pedestrian poles locations  
 11/14/22 - 11/18/22 Gerelco (signalization contractor) progressing with installation work. Directional boring ongoing north of NE 14th street by Viking crews  
 11/20/22 - 11/24/22 2nd Crew is working near riverside drive (project limits). 1st Crew working on the project south end and pulling cable near NE 5th Street restored. FPL crews are also progressing with poles installation along the corridor.  
 12/05/22 - 12/08/22 Crews have been working on splicing fiber cables and conduits at new pits. MOT is place to regulate vehicular and pedestrian traffic  
 12/12/22 - 12/15/22 2nd Crew has now moved next to the bridge abutment and working on new excavation/trenching 12/19/22 - 12/22/22 Contractor working on restoration activities including asphalt patched and new concrete sidewalk flags. Cleanup of the construction zone is progressing ahead of the holiday season.


### CONCEPTUAL ELEMENTS



Undergrounding overhead utilities on SR A1A from Terra Mar Drive to Hillsboro Inlet to reduce power outages during storms and improve the aesthetics of the corridor.



Improvements to include sidewalk widening, designated bike lanes, lighting, and raised median.

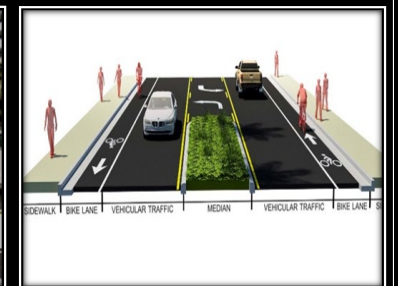

### PROJECT SCHEDULE MILESTONES

#### CONSTRUCTION:

Undergrounding Utilities Conversion work	Start :February 2021 - End March 2023 (Phase 1)
Undergrounding Utilities Conversion work	Start :May 2022 - End December 2023 (Phase 2)

Actual Streetscape Construction activities for Phase 1 are scheduled to begin early November 2022 and end December 2023

Phase 2 Streetscape construction activities are tentatively scheduled for Fall 2023

### PROJECT SITE LOCATION



**TOTAL LENGTH: +/- 3.2 Miles**

**PHASE 1:** Terra Mar Drive to East Atlantic Boulevard (construction complete 09/30/21)

**PHASE 2:** East Atlantic Boulevard to Hillsboro Inlet (construction complete 10/01/24)
