

## June-July 2022 Project Dashboard

### Project 19353 A1A Streetscape Improvements

#### Prime Consultant:



#### CMAR:



#### City of Pompano Beach

**GO BOND DIRECTOR:** FERNAND THONY, PE

**PROJECT MANAGER:** FERNAND THONY, PE

**CURRENT PHASE:** CONSTRUCTION

**DESIGN TEAM:** KEITH

**CONSTRUCTION TEAM:** BURKHARDT

**APPROVED BUDGET:** \$19,925,294.55

#### CONSTRUCTION PROGRESS




#### PROJECT OBJECTIVES

The SR A1A Streetscape project involves various improvements from Hillsboro Inlet to Sunset Lane (South of Terra Mar Drive) such as undergrounding overhead utilities to reduce power outages during storms and improve the aesthetics of the corridor. Additional improvements include new sidewalks, bike lanes, traffic calming features, roadway resurfacing, lighting and landscaping. The Project will be broken into 2 Phase 1 - Phase 1 will address the roadway segment South of Atlantic Blvd while Phase 2 will encompass the roadway north of Atlantic Blvd.

#### PROJECT UPDATES

Overhead Utilities Conversation Project Activities: Over the past 2 months constructions activities are progressing as per below:

6/1/22 - 6/3/22: Directional drilling from 6th St to 7th St (Comcast & FPL); Setting vista cabinet concrete pads  
6/6/22 - 6/10/22: Tying in ATT and Comcast; still directional drilling from 6th St. to 7th St. (ATT and FPL)  
6/13/22 - 6/17/22: Tying in feeder conduit at 6th St.; Directional drilling from 7th Pl to 8th Ct. (FPL Primary and Feeder)  
6/20/22 - 6/24/22: Tying in Comcast; Directional drilling from 8th St. to 10th St. (FPL Primary and Feeder)  
6/27/22 - 7/1/22: Set Vista Cabinet Pad at 7th St; Directional drilling across A1A at 7th and across 10th (FPL Primary and Feeder)  
7/5/22 - 7/8/22: Directional drilled from 10th St to 12th St. (FPL Primary and Feeder)  
7/11/22 - 7/15/22: Tying in FPL to 12th St.; Set ATT Manhole at 10th St.; Directional drilled at 5th St (ATT)  
7/18/22 - 7/22/22: Directional drilling from 5th St to 7th St. (ATT)  
7/25/22 - 7/29/22: Set ATT Manhole at 12th St.; Directional drilling from 7th Pl to 7TH Ct. (ATT) and Directional drilling from 13th to 14th St. (FPL)

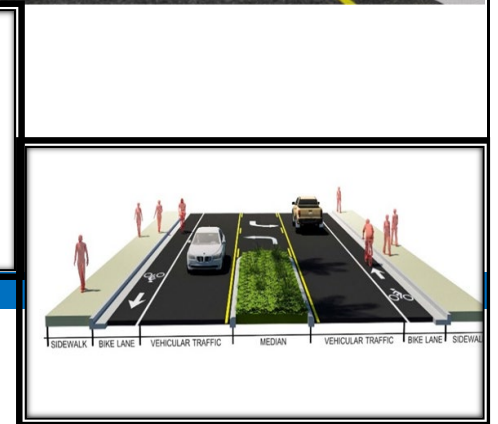

#### PROJECT SCHEDULE MILESTONES

##### CONSTRUCTION:

Undergrounding Utilities Conversion work	Start :February 2021 - End March 2023 (Phase 1)
Undergrounding Utilities Conversion work	Start :May 2022 - End December 2023 (Phase 2)

Actual Streetscape Construction activities for Phase 1 are scheduled to begin September 2022 and end December 2023

Phase 2 Streetscape construction activities are tentatively scheduled for Fall 2023

#### PROJECT SITE LOCATION



TOTAL LENGTH: +/- 3.2 Miles

**PHASE 1:** Terra Mar Drive to East Atlantic Boulevard (construction complete 09/30/21)

**PHASE 2:** East Atlantic Boulevard to Hillsboro Inlet (construction complete 10/01/24)
