

Prime Consultant:



CMAR:



City of Pompano Beach

GO BOND DIRECTOR: FERNAND THONY, PE

PROJECT MANAGER: FERNAND THONY, PE

CURRENT PHASE: CONSTRUCTION

DESIGN TEAM: KEITH

CONSTRUCTION TEAM: BURKHARDT

APPROVED BUDGET: \$19,925,294.55

CONSTRUCTION PROGRESS



PROJECT OBJECTIVES

The SR A1A Streetscape project involves various improvements from Hillsboro Inlet to Sunset Lane (South of Terra Mar Drive) such as undergrounding overhead utilities to reduce power outages during storms and improve the aesthetics of the corridor. The undergrounding work portion comprises two (2) phases: South of Atlantic Blvd and North of Atlantic Blvd. Additional improvements include new sidewalks, bike lanes, traffic calming features, roadway resurfacing, lighting and landscaping. The Streetscape per se Project also comprised 2 Phases. Phase 1 will address the roadway segment South of Atlantic Blvd while Phase 2 will encompass the roadway north of Atlantic Blvd.

PROJECT UPDATES

Undergrounding/Utilities Conversion:

Contractor has been active along the segment between 7 street to approximately 12 street. Crews have dug new pits and directionally installed new conduits for the future street lighting. Additionally, all excavations, pits and damaged sidewalks are being restored. Crews also performed remaining tie-ins north of 14th street for recently installed utilities conduits.

Streetscape Improvements:

Phase 1 - Contractor has completed installation of the decorative brick paver areas. Work has begun on the new landscaped medians. To date, asphalt pavement was sawn and top limerock material hauled away. Concrete curbs have been outlined, formed and placed pending for new planting soil to be backfilled at the new planters. FPL new light poles installation has been temporarily halted due to material back order delays.

Phase 2 - Plans final review completed, consultant is now waiting on approval from FDOT.


CONCEPTUAL ELEMENTS



Undergrounding overhead utilities on SR A1A from Terra Mar Drive to Hillsboro Inlet to reduce power outages during storms and improve the aesthetics of the corridor.



Improvements to include sidewalk widening, designated bike lanes, lighting, and raised median.

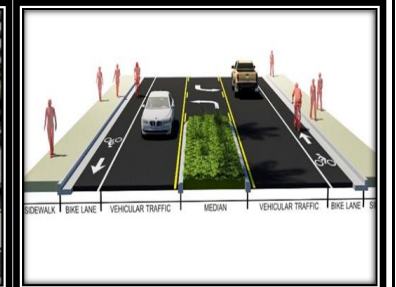

PROJECT SCHEDULE MILESTONES

CONSTRUCTION:

Undergrounding Utilities Conversion work - ongoing

Start :February 2021 - End March 2023 (Phase 1) completion delayed due pending FPL switching orders - new projected date Nov 2023

Undergrounding Utilities Conversion work - ongoing

Start :May 2022 - End December 2024 (Phase 2)

Phase 1 Streetscape construction activities ongoing (and originally scheduled to end December 2023)

NOTE: Project will be impacted by FPL delays and completion will tentatively be pushed back to April 2024.

Phase 2 Streetscape construction activities are tentatively scheduled to begin in Spring 2024

PROJECT SITE LOCATION



TOTAL LENGTH: +/- 3.2 Miles

PHASE 1: Terra Mar Drive to East Atlantic Boulevard (construction complete 09/30/21)

PHASE 2: East Atlantic Boulevard to Hillsboro Inlet (construction complete 10/01/24)

