

October 2022 Project Dashboard

Project 19353 A1A Streetscape Improvements

Prime Consultant:



CMAR:



City of Pompano Beach

GO BOND DIRECTOR: FERNAND THONY, PE

PROJECT MANAGER: FERNAND THONY, PE


CURRENT PHASE: CONSTRUCTION

DESIGN TEAM: KEITH

CONSTRUCTION TEAM: BURKHARDT

APPROVED BUDGET: \$19,925,294.55

CONSTRUCTION PROGRESS

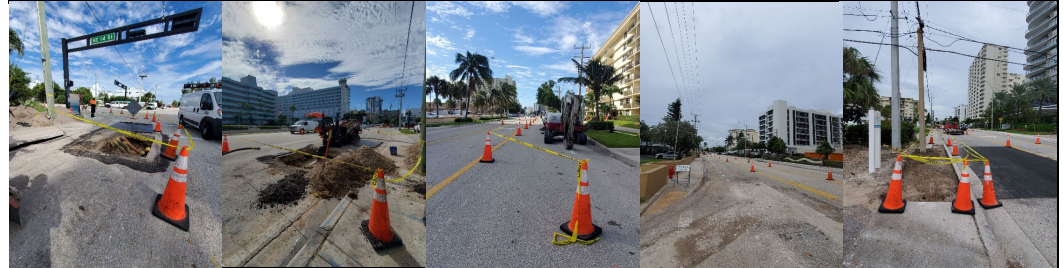

PROJECT OBJECTIVES

The SR A1A Streetscape project involves various improvements from Hillsboro Inlet to Sunset Lane (South of Terra Mar Drive) such as undergrounding overhead utilities to reduce power outages during storms and improve the aesthetics of the corridor. Additional improvements include new sidewalks, bike lanes, traffic calming features, roadway resurfacing, lighting and landscaping. The Project will be broken into 2 Phase 1 - Phase 1 will address the roadway segment South of Atlantic Blvd while Phase 2 will encompass the roadway north of Atlantic Blvd.

PROJECT UPDATES

Overhead Utilities Conversion Project Activities: In October, construction work progressed as per below:
 10/1/22 - 10/4/22 MOT has been extended just south of NE 14th St. The southern limit of work is now around NE 8th street. 1st field crew is moving ahead with boring and laying sleeve conduits.
 10/7/22 - 10/11/22 Utility sleeves for AT&T and Comcast continue to be joined at interconnecting points. Pits are being backfilled sequentially and some restorations work is taking place.
 10/15/22 - 10/17/22 2nd Crews performing directional borings near NE 14th St. All traffic is routed to minimize backlog at the intersection.
 10/14/22 - 10/18/22 Crews resumed work on excavation plate patches at some locations. At other locations, pits within traffic lane are backfilled and restored. Crews are also moving to splice the newly laid sleeve conduits. Work limits has been extended northward.
 10/21/22 - 10/25/22 Additional restoration work is taking place. Some of the newly restored areas have been re-opened for public use. Southern work limit has moved beyond NE 9th street. MOT is adjusted daily to address traffic flow and vehicles are shifted accordingly along the impacted road segment. Viking crews progressing with sleeve conduits for AT&T and Comcast utilities.

PROJECT SCHEDULE MILESTONES

CONSTRUCTION:

Undergrounding Utilities Conversion work	Start :February 2021 - End March 2023 (Phase 1)
Undergrounding Utilities Conversion work	Start :May 2022 - End December 2023 (Phase 2)

Actual Streetscape Construction activities for Phase 1 are scheduled to begin early November 2022 and end December 2023

Phase 2 Streetscape construction activities are tentatively scheduled for Fall 2023


CONCEPTUAL ELEMENTS



Undergrounding overhead utilities on SR A1A from Terra Mar Drive to Hillsboro Inlet to reduce power outages during storms and improve the aesthetics of the corridor.



Improvements to include sidewalk widening, designated bike lanes, lighting, and raised median.

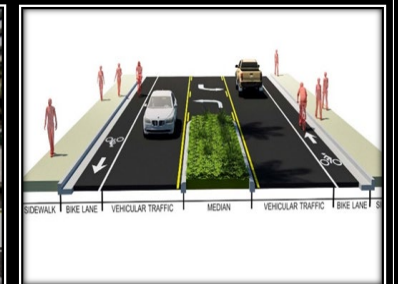

PROJECT SITE LOCATION

