

August/September 2022 Project Dashboard Project 19355 Dixie Hwy Improvements

Prime Consultant:

Kimley»Horn

CMAR:

WT
WHITING-TURNER

City of Pompano Beach

GO BOND DIRECTOR: FERNAND THONY, PE

PROJECT MANAGER: FERNAND THONY, PE


CURRENT PHASE: CONSTRUCTION

DESIGN TEAM: KIMLEY HORN

CONSTRUCTION TEAM: WHITING-TURNER

(Segment2) APPROVED BUDGET: \$45,632,432.00

CONSTRUCTION PHOTOS (SEGMENT 1 COMPLETED)

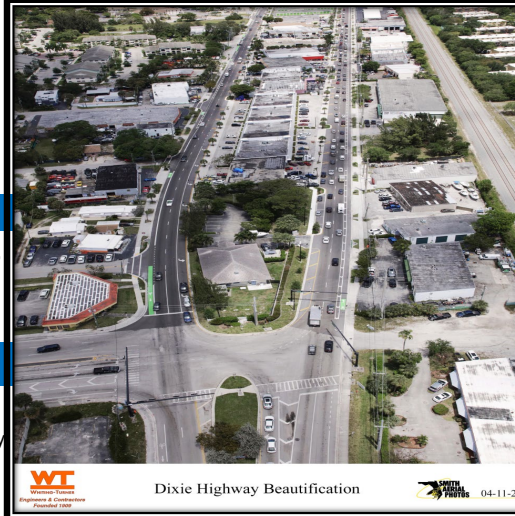

PROJECT OBJECTIVES

Upgrade the Dixie Highway corridor from McNab Road to Sample Road, including roadway crossing improvements, bicycle lanes, medians, sidewalks, lighting, landscaping, street furniture and other streetscape improvements. Project comprises 3 segments. Segment 1- Mc Nab Road to SW 3rd street (completed). Segment 2 (SW 3rd street to NW 10 Street) and Segment 3 (NW 10 street to Sample road).

PROJECT UPDATES

Work on Dixie Highway south of Atlantic Boulevard (Segment 2) is complete. The CMAR is concentrating on permitting efforts to start work north of Atlantic Boulevard (Segment 3). The agreements with the CMAR and County (for Surtax) have been completed. City is awaiting to receive approvals of Interlocal Agreements. Purchase Orders have been issued.

PROJECT SCHEDULE NOTES

Segment 2 work will be broken along the two main axis :

Atlantic Boulevard (work limits) from approximately NE 6th Avenue to NE 2nd Ave/Cypress Road
November 2022 to December 2024 (substantial completion)

Dixie Highway work from SW3rd Street to NW 10th Street
November 2022 to December 2024 (substantial completion)

PROJECT SITE LOCATION



Partial Site Rendering - Atlantic Blvd. from Dixie Highway to Cypress Road

