

Prime Consultant:



ITB:

City of Pompano Beach

CIP MANAGER: Dr. TAMMY GOOD, PMP

PROJECT MANAGER: Anthony Alhashemi, PMP/Dr. Tammy Good, PMP

CURRENT PHASE: REDESIGN

DESIGN TEAM: WALTERS-ZACKRIA ARCHITECTS

CONSTRUCTION TEAM: TBD

APPROVED BUDGET:

TBD

CAPITAL PROJECT RENDERINGS



PROJECT OBJECTIVES

A new park, including soccer/football field/running, concession, and restroom building, parking & landscaping to be located adjacent to Apollo Park

at 1580 NW 3rd Avenue

PROJECT UPDATES


Project updates: DRC Review is complete. The project has a Development Order (8-2-2023). The project scope was evaluated and now includes a running track, added parking spaces, and cooking kitchen. Purchase orders are currently being issued to accommodate redesign of scope.

PROJECT SCHEDULE MILESTONES

DESIGN PHASE: Begins September 2019 Ends: May 2025 Complete

CONSTRUCTION PHASE: Project is being redesigned to include a running track - New start date: February 2025

PROJECT SITE LOCATION

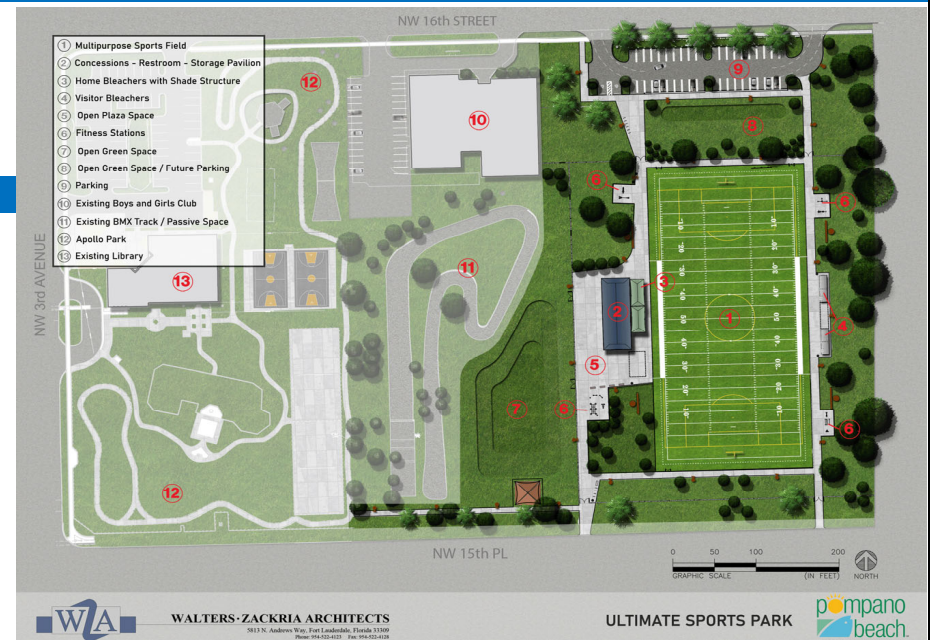

WALTERS-ZACKRIA ARCHITECTS
3813 N. Andrews Way, Fort Lauderdale, Florida 33309
Phone: 954-522-4331 Fax: 954-522-4334

ULTIMATE SPORTS PARK
